WALTER SCHLEIF
GOLD LOGBOOK

PX-751

First Aid Rm 51 Dey Street
"Ext 51 - when closed
call SU-2-1290

Beekman Hosp BE-3-8300

W. SCHLEIF

400 Curtain Wall
Column Covers

110 Carpentry. Dry Wall
A-AB 213
Install Doors. A-AB-213-A

113 Spraying Capes on Trusses

107 Resilient Tile floors

106 Marble

109 Wall & Floor Tile

Bert Weinstein 11 floor sec.
964-8691

Mario De Bona 732-5222

Star Circle 349-7380

3-31 9-30
4 31
5 31
6 31
7 31
8 31 3-31-70

STEWART

At Personnel -
At Job Site 11 AM - sent to 2nd floor to await Ed
Told to go with Jim to get aquantaten with Job

4-1-70

Same as above.
Application of Epoxy to adhere Asbestos to columns.

4-2-70

to Personnel to have Prints & Photos & Issuance of ID Card to Job Site 10 AM -
the application of Epoxy & the coating of Asbestos is questionable I believe that everyone is trying to hang their hat on any thing that they possibly can to come up with a solution to this problem.

4-8-70

X = Metal above Roof
Problem setting Hasp

On East & West Stair Forms have Bumper Holes - Center Stair has none - Specs Call for all - What is deviation? -

4-8-70
Gauge made out of Tubing to "undersize" to check Hammell Forms. #1 & 2
Gauge 3/16 under for Center #3

	EAST	Center	WEST
18	1/8 -	OK	OK
17	1/8 -	OK	OK
16	OK	OK	1/8 -
15	OK	OK	OK
14	1/8 -	OK	OK
13	OK	OK	1/8 -
12	OK	OK	1/8 -
11	1/16 -	NG 3/16 -	1/8 -
10	1/8 -	OK	N.G.

Sheet Rock Problem - Distance between BB on Forms = 3 7/8 -

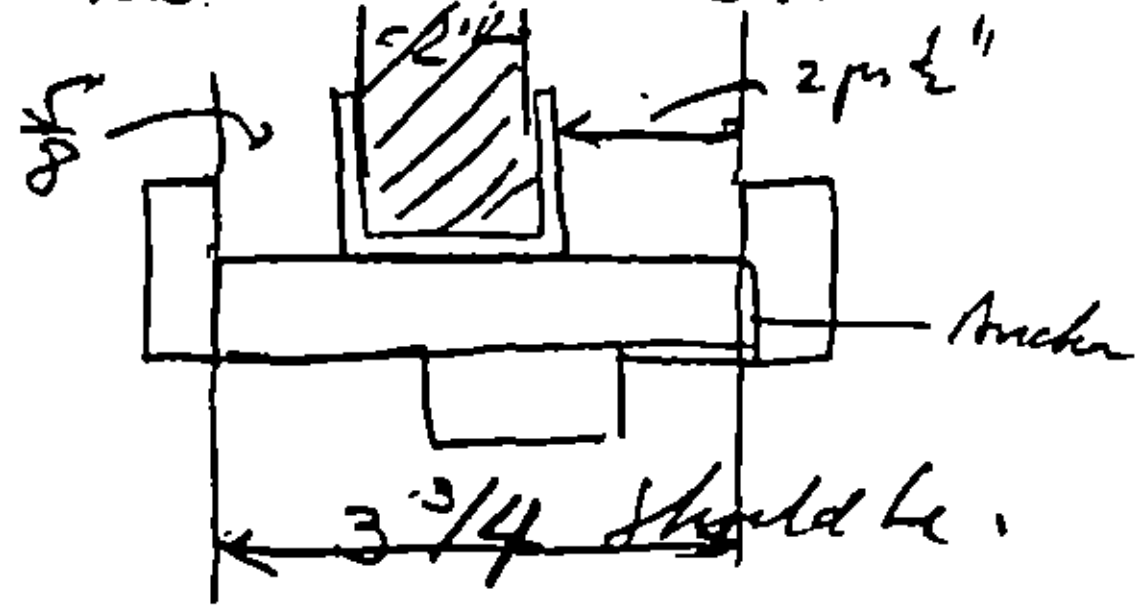

4-9-
16 floor SE Elevator Shaft
first layer of Shaft Rock some
panels are not Contact to concrete
app 2" short top - Bottom they
are filling in Voids with Pcs.

NE Elev Shaft Corridor poor
workmanship on Core Board
They are cutting both Core Board
& Channels to some length
and shimming up Bottom
to Hang on to top this is also being
done at other site
18th floor N W Shaft Hoisting
cables in concrete .. Star Circle
are notching J" Runner and they
will have to notch Core board
to pass cables.
Bolts on Elev Header to Struts
are running into Corridor thereby
Star Circle have to cut the Core
Board to fit if bolts were Elevator
removed into shaft this could be

4-10
Spoke to Tom - Star Circle Re this last
of Core Boards - He instructed his
men to conform to spec -

Fair

4-11 Sat

SW-12 - Painter 12
Iron Workers 5
Col Conn Corp 38+

Note: 11 Col Covers EPONOL did not dry - even overnight they are going to strip with MEK & R[illegible] -

NE-12 Painter 9
Iron Workers 5
Col Conn Corp 55
Spraying Capco on Columns - EAST

NE 14 Painter - 18 + 1 foreman
Iron Workers - 4
Col Conn Corp - 60
Spraying Capco on Colums EAST - South

Painters total (32 + 1 foreman) Col
Iron Workers 14 Covers
4 Caulking CC

15 floor Setting up for Monday

1 floor 19 Covers Epoxol did not Dry Starting

4-11

34th fl Barricade down on North End of Elevator 6-7 - by Ulimit
Temp Bars put across front

41st fl 2 men spraying Capco on Beams & Trusses

55th fl 2 men spraying Trusses
3 men Hanging Tarps

9th fl NW - 4 Iron Workers Cleaning out Caulking Pocket on Col Covers. Patching Capco on N Side

10th fl - MEK Test in Safety Cans ?

DeBona total 400
1 Supt
2 Foremen
13 Mech
2 Engineers
23 Labor
113
1 Foreman
4 Mech
12 Labor

4PM

4-13-70 FAir 110

See 4-8

110

4-14-70 FAIR
TUESDAY

20th floor West Stairwell -
Buck set for 1/2" ~~[illegible]~~ on Stairwell
& 1" on Corridor - They must
use 1/2" SR on Stairwell instead of
5/8" 2 pcs 1/2" SR on Corridor - Doyle
being set now.

4-15-70 F/fri
West Stair
20 fl Mock up of Door Frame
using 1/2" Sheet Rock Stair side
& 2 pcs 1/2" Sheet Rock Corridor
side - Tight fit.

4-16-70 -

Sam of Star Circle Stated that he
Cannot Wait for extra Testing
or his office he is going ahead &
setting Bucks as sample. 20 fl W
Spoke to Lucarelli & Sam. They
would contact the proper parties
to see about changes - then advise

Cov Board. Elect Closet 35 fl.
Buck to check 23 floor STL
Spraying Capco on Truss 41 fl.
Sodding Taps 37 fl.
Spraying Capco on Truss 36 fl
Removing Taps 35 floor

4-17-70 Fair

Protection on El Shafts - does this pertain to every floor or every other floor?? If every other floor should it be Planked Complete

---

4-19-70 #1817

1 Foreman

1 Steward 8-5:30

7 Cpt -

Sunday

4-20-70 Rain

Safety With Fred Stuyvesant - to Dic Underhill - Spoke to Sid Philips Contract Supt at office - 47th floor. 3 Shafts open 38-39-40 - We are to speak to Don De Paulo Dic Mick Foreman Forman - Cindy Barbara

24 floor Wire Raceway into corridor Rock-lath not going in True - They also Remove 1" of Rock 30 Shaft - Spoke to Warren Marklut Tishman

Stair West 17-18-19 out - Spoke to

Shafts 7-8-9 floors 12-13-14-15-17-19 Reamed for saddles - no saddles Called for - Dic to fit - Warren told

Shaft 20-21 Concrete forms - 17 fl not removed - Warren told.

4-21-70 ~~Fair~~ Cloudy

DiBona Tarps taking down on 41
Tarps going up on 39
Tarps up on 38-
37 fl Tarps up 50% Cap on Trusses
Wait spraying - Stop - 3 men cleaning floor.
Hanging Tarps outside N-S-W Elev 26 floor.

Star Circle Started Setting Frames in Elect Closet 36 fl N 33 fl N. using Buck # AER1 holding ½" inside & ~~[illegible]~~ 2 pcs ½" outside wet 2" core Should be 5/8 inside See Shop # 59 FCA details
Star Circle Missed few clips when shooting in 'S' Chan 21 fl NE Shaft - 20 fl North West Shaft 17 fl opp Center Stair

4-22-70 Fair
AER
37 NE Elect Room - Sides No Buck
36 With Buck
35 " "
34 No Buck
33 With "
32 With "
31 S & H Sect only
31 SW S-H Sect only
26 NE Sides No Buck
25 " " " "
24 } None
23 }
22 NE Sides No Buck
23 Setting Stair Well Bucks - Also set 22-21-20-19-18-17-16-15-14-13-12-11
AJR
Telephone Rooms started 3 Sides No Front Walls or Door Frames Can be Set - There is no Steel Stud Part on Job.

4-23-70 Lea Rain

1PM
Spoke to Fred Corrado (Tishman) Re 41 fl that De Bono sprayed bottom of Beams that the Steamfitter are complaining that in their removal the Cafco is going down their Boots & they itch - after they take a Bath. Fred was surprised that they take Baths. He is going to contact De Bono to Respond - at 4 PM checked with Fred & he could not get in touch with De Bono - Will Try tomorrow AM.

Notified by Tom of Star Circle that They are working Saturday 4-25-70 on Shaft #39-40-41 with Core Board & Rock where required from 40 then 3 Crews 1 at middle, 1 at Bottom Will work till they complete

4-24-70 Cloudy Rainy

Spoke again to Fred Corrado he was still unable to get an answer from De Bono Regarding Spray Beams 41 fl.

Contacted by Star Circle Re Sat Work - 4-25 They Will Start on 40 fl Shaft # 39-40-41 & complete Core & Sheet Rock - a Crew of 40 men are anticipated

Spoke to Star Re short Core Board - No Shims Will be tolerated -

4-25- Fair
Sat

Star Circle working on Shafts #39-40-41 from 39 down to 18 Installing J & H channels Installing Core Board & Sheet Rock 1 Supt. 1 Asst Supt 3 Foreman - 1 Shop Steward - 1 Coffee Boy 38 Men Total 45 Men Sat.

On 39 fl. Shaft #40 Frank VAGNINI while using Star Stud Driver on J channel on floor slipped and shot through his left palm. Man was taken to Hospital by Port Doctor & Bladen of Star Accident occurred at 10:20 AM

Trusses sprayed above 28
28-29-30-31-32-33-34-35-36
50% Comp - 37-41
Tarps up ready to spray 38-39
No Tarps on 40.

4-27- Fair
Mon

Inspected Core Board Installation found many places where fire stop & adjacent walls not tied together - Spoke to Sam - he asked me to mark spots with (S) & he would send some one to correct some there are locations where Core Board is short

4-28- Fair

Marked all Location on Core Board from 10 to 38 Inc where Tie in- [illegible] were left out Star Circle is following up and inserting some

Questioned location of Elevator frames in relationship to Core Board - Letter from B. Wernsting to Star Circle to hold 2 1/2" between edge of Buck to Core Board to [illegible] support, Room for Marble. Letter Dated April 26.

Met With Joe Iacovelli of Star re payment he made appointment to meet With Mr on Thursday 1PM.

Seidon shipped Material today to Frame # ATR-1 - AWTR-1 - AU401 AC005-1 - plus 43 Sills for Tele & Electric Closet - (Loan)

4-29 Fair

38 floor Shaft 42 Corridor "H" Section Left out between 2 pcs Core Board for Removable at later date

Otis is resetting Bucks on 15 floor Shaft 29-28-27 & Setting doors. they are shimming Buck & Plumbing & racking and Screwing into Core Board & "C" Channel Note: No sheet Rock has been put on there as yet

Shaft #5 Will be Screened in from Lobby to 39 some ~~Shafts on~~ floors will have Core Board when possible

Dr Bona received new Material Capco today. started Spraying Columns Will start to Spray Trusses when he receives more material.

4-30 Cloudy

N = No
P = Partial
C = Com

Fl	Core Board (on floor)	Sheet Rock	Layout	Stair Bucks	J Elec only	NE Elect NO Board	Tel	HA SW
40	N	N	P	N		P	N	N
39	Y	Y	Y	N	00/40	P	N	
38	Y	Y	P	N	N	N	N	
37	Y	Y	P	N	00/40	P	N	
36	Y	Y	Y	N	00/40	C	N	
35	Y	Y	Y	N	00/40	C	N	
34	Y	Y	Y	N	00/40	C	N	
33	Y	Y	Y	N	00/40	C	N	
32	Y	Y	Y	N	00/40	C	N	
31	Y	Y	Y	N	00/40	C	N	
30	Y	Y	Y	N	N	N	N	
29	Y	Y	Y	N	N	N	N	
28	Y	Y	Y	N	N	N	N	
27	Y	Y	Y	N	N	N	N	
26	Y	Y	Y	Y	S	Y	N	P
25	Y	Y	Y	Y	S	Y	N	N
24	Y	Y	Y	Y	P	N	N	N
23	Y	Y	Y	Y	P	N	N	P
22	Y	Y	Y	Y	P	N	N	P
21	Y	Y	Y	Y	P	N	N	P
20								

5-1- Fair

Otis men Setting Bucks Plumb & Jointing to Core Board using shims and straps where required Then Hanging doors -

Has Running Protection both Shearing & Core Board

Saddles being grouted 25 down

5-4--70 - Cloudy 50°

Met [illegible] Elza Arch
Westmore To 7 Completion
then checked out with
Boris & Iacinelli
Tower A & B -

5-5-70 - fair

50°

Checked All Door Frames in
Specimens at Hinge Joint 40 &
Reod - (101) per

De Bona Starting [illegible] Tower
on 27 floor. ~~NW Elevator~~
& closing from core Tower
38 fl -

CONTRACT NO.	CONTRACTOR	WEATHER
113	D. Bono	Fair

Status of Floors

41 fl Trusses only No Core col	25%
38 " " " " "	15%
37 " " " " "	25%
31 to 30 Inc " " "	50%
29 to 9 Inc Truss & Core Col	70%
8 Core Col only Truss not done	20%
7 fl Core Col only - No Truss on floor	80%
6 fl Core Col only Truss not Done	20%

[illegible] — 5-6-70 — Day

INSPECTOR — DATE — SHIFT — REVIEWED BY

INSPECTOR'S DAILY NARRATIVE

2 of 2

CONTRACT NO.	CONTRACTOR	WEATHER
113	D. Bono	Fair

5 to 2 Inc. Core only - No Truss on floor — 80%

Note - I have given 65% for Trusses & 35% for Core Col and have deducted from Truss %. 5% for PT Cell, 5% for Dampening unit Connectors & 5% for Visuals & Holddowns on Core Col deduct % 7 5% for Visuals & Holddown & 10% for insufficient [illegible]

[illegible] — 5-6-70 — Day

INSPECTOR — DATE — SHIFT — REVIEWED BY

Fair
Cool

~~Top Plate Bus Pe~~

5 floors / wk

Core Board 3 floors / wk

Layout 5 floors / wk

Boris 40 -

See Special Report dated 5-7-70 on De Bona - Fred Coronado - Bert Vicentin Re 41 fl - Bott of Beams Scraping for Bond Counter

5-7-70 - Fair

(110)

21 fl 2 Men Inst Plank
22 fl 12 Men Inst Plank & Shot
23 6 Men Inst Plank & Shot
22-23 3 Men Pick up forming
22-23 3 Men Protection
25 2 Men Forming Machine Room
24 2 Men Inst Studs
26-27 28-29 2 Men Bott & Top Track Stairs
31 5 Men Top Track
30 1 Man Bott Track
16-17-18-23 - 4 Men Inst Plank El Shaft #5 Bott Lug
26 2 Men Layout Mach Room
22 to 34 6 Men Protection
2 Men Coffee & Pick up Material
2 Men Labor
3 Foreman
1 Asst Super
1 Super

58 Men

Bucks Rec FDC
AS044
AS042
AS045
AS043

4:30 Sat to 12 Mid

6
7
Shaft

1 Hose Elbow 16 to 34 All day Sunday

May 8-70 - Fair

23 14 men Inst Plank & Sheet
22 4 men Inst "
22-23 2 men Pick up forming
22-23 4 men Protection
32 fl 2 men Plumb for top track
32 - 4 men Inst Top Track
31 1 man bottom Tracks
" (2) men setting Bucks
" (1) man framing stairs
25 2 men framing Top & Bot Track Motor Room
25 4 men Cutting studs
6 fl 2 men Layout
37 2 men Layout
2 Labor
4 men Removing Protection
2 men Coffee & Pick up Mat
21-22-23 2 men Install Bucks, Plank North - South Elect Closet
3 Foreman
58 men 1 Asst Supt
1 Supt

May 9-70 Sat Fair
3:30/12:30
Star Circle Stripped Protection Shaft #6-7 - on South East Wall Installed Scaffolds - Top - Bott Track - H Section & Completed 4 floors With Core Board & Sheet Rock for 10 to 32 Inc

(35)

30
1 Lab
4 Sup.

(35)

5-10-70 Sun.
Fair

25 floors done
10 to 34 Inc

Rem Pert
Layout
T-B Track
H
Core
Sheet Rock
Rem Plank
Close up

} Average 18 men
Average / floor

26 Men
4 For
1 Hstp
1 dS
32 Men

4 Men Worked to 10 PM
Sunday Cleaning Shaft & top of Cab

5-11-70 Mon
Fair

78 Sheet Rock Del & Dist on floors 9 to 16 Inc.

113 Contract as per Jimmy Blue Eyes - No Work on this today.

Otis Claims they will join Car #5 to Start to construct Temp Enclosure Tuesday 5-12-70
It Will take then two days to Construct this Cab.

Shaft #6 - East Wall been off Channel Welded to Column
24 Plank & Sheet
23 Plank & Sheet
23-24 Protection 10 to 34
33 Top Track
32 Frame Stairs & Backs - Bott Track
25 Framing Mach Room
26 Joint Studs
6-5-37 Layout
23-24 - Plank East Clos NES

60 Men

5-12-70 Fair
Tuesday

113- Started 1 PM on keying Bolt flanges of Beams on 41 ft North Side over shaft.

Plumber scaffold being set up. South East 41 ft

44- Layout - 45
45-46-44-47 Cutting Studs
33 Plumbing Top track & Top track
24-27- Forming Shaft -48-35-37-38
26- Int Studs
23-24- Plank & Sheet
24 Pick up forming
25 Int Plank
23-27 Protection
34 Forming & Plank Elevator Clos
58 Men

5-13-70 Cloudy RAIN
Wednesday

5 P Core - Water 9 to 16
5 P Core Plaza 10 to 13
41 ft No Activity 8 to 10 AM
Spraying Team 39
Car # 5 - Union & Ulrs is going to move material from in front of each floor opening

34- Plumbing Top track & Int
27 Studs & Forming Elev Beams
25-26-27-28- Plank Shaft 37-38
24-25-26-27-28 Pick up forming
24 Plank & Sheet
25 Plank & Sheet
25-30 Protection 58
44-45 Layout

Car 6-7- Rails up to 55

---

29 floor Stair Pit West Stair Removed fold hats

5-14- Cloudy

Sample Elev Back 16 floor
With Sheet Rock shafts 28-29
Sample Elect Closet 32 fl
South West - Sheet Rock

113 Spraying Trusses 39
Scraping 41 - 2 men

35 - Plumbing Top Track & Inst Top Track
27 Studs
34 Inst Backs & Forming Stairs
44-45 Layout
45 Foreman
24 Inst Plank & Sheet
24-25 Pick up Forming
25 Inc Plank & Sheets above 26
~~26~~ 8 Men on Protection
total 58 men -

(5-15-) Friday Fair

(113)
Scraping Bath Floors of
Beams 41 fl 2 men
17 Comp NW
12 1/2 Comp SW

(110)
Top Track - 36
Plumb Top Track 36
forming Stairs & Backs 33
forming Elev Shaft 24-25-26-36
Inst Studs 27
Layout 45-46
Const Helper 39 fl.
Plank Elect Closet & forming
Plank & Sheet 25-26
Plank Elev Shaft 36 - 24-25-26
Pick up forming 25 - 26
Inst Plank 27
Protection 8 men
total 58 -

5-18-70 Monday
Cloudy - Rain

113
5-16 - Sat 2 Men Scraping Bott of Flanges on 41 fl - as per Jimmy Blue Eye. All flanges are scraped except 3 - could not get them - has 2 men cleaning floor near Star Circle - As of Friday 5-15-70 No 4" SR is to be used over joint Boards - Tape should be used - SC has contacted Bert Clements for change on this - SC Has not as yet received order to use dashes under Heads of Fans.
Checking on Why ASTR3 Beams do not have silencer Holes in steel Joint? -

5-19 - Cloudy
Later Rain

110
26 fl Plank & Sheet & Pick up Scrap
27 Plank & Sheet
29 Plank
38-5 - Layout
39 Loader
27-28-29 Forming Shaft 39-40-41
29 Inst Studs
36 Forming Stairs
38 Plumb Top Track & Inst Top Track

113 - Spraying Caps on Trusses 39 floor
Cleaning 41 floor.

Tishman gave Stan 4 Men to clean floors ahead of Layout as follows · 2 are on 5 - 2 on 38

5-20-70 Fair

Color of ounceast green - As per Jim Osborne - to be started - Monday 25-70 -

Port 113
110 1/2 Day

Parade today -

Gave Mem to
Fennell on 32 ft Elect Cl
Fed Connell on Dec to Chip
for Marble 10 ft
to Osborne - to Cover Eq.
& not to spray back flag
on Machine Room

5-21-70 Fair

113
41 ft. East Center Elev
Cing Scraped

Spraying Beams 40

Elevator Bucks Re - Core Wall



x Started 2 1/2"
x Changed 2 1/4" up to x
x Changed 2 1/2"
x Changed back 2 1/4" ?

Layout 4-5-39
Lobe & Plonking closets Elect
Plank & Shutrack 27-28
Pick up forming 28
Plank Stairs 30
Plumb Top Track 39
Inst top Track 39
Inst Studs 30
Forming Stairs 36 52 men

5-22-70 Friday
Fair

Bud Newton
Norfolk - Note Meeting on Subject
4" Spray Proof - Non Men
2 1/2" Elev Forms - Stay as is -
32 ft Sample

Ornament Color is Blue

Layout Mach Room 17-18-19-4
Layout 39-40
Pp Butt Track 35-36-37-38 -
Framing Doors El. 37-38-28-29
Inst Studs 30
Pp-Butt Track Mach Room 17-18
Block Shattuck 28-29
Block - 30
Pick up framing 29
Block - Staff 37-38 - 29-30-31

Staff 5-22 Cont
H35 Temp Pert Comp
42 Car operator Came 8:50
Car not Working - otis
Men Working Trying to Start
Floor are not cleaning
Rack - Plumb Elev Bucks
& Hanging Doors 11 floor 24-25-26
Marble Men Removing & Re
Caulking 10 ft Joints at Elevator
& Bucks - Boozer
Frank Holtzman had Don
DePaulo of Dic on Floor to
Chop Recess for Marble Don
stated that he would have
men on floor this Afternoon
Protection in Elev Doors & Jams
removed - have otis Protect
their Work -
Spraying Beams 40 ft 1 Man
1 Man Cleaning
1 Man Chopping Recess
1 ft for Marble Base This
Afternoon

5-25-70 Cloudy Rain

11 Spraying Blue overcoat 11 floor S W Corner. Color very pale - Di Brose will add more coloring to make Darker

Layout 40-4
Planking Top Track -39-40
Forming Stairs 38-39
Bolt Track 33
Set Studs 31
Forming Motor Room 18
Plank & Sheet 29-30-31-32
Pick up forming 30
Set Plank 31
Protection 29-30-4-5

43 Cpt
2 Lab
2 Apprentices
1 Steward
3 Foremen 1 Ast Supt 1 Supt

(53) Prd.

Marble - None

Vir of Sta
26 Cpts - 1 Foreman

DeBose - 2 Sprayer Overcoat
1 Sprayer Cafe
1 Labor Cafe

5-27-20 Fair

113 - Blue overcoat sealer
5 gal Cafco Bond Seal
15 gals Water
~~2 contain that Blue affalys~~
~~6 Hot Raffic Cor~~
200 oz Coloring Chromium Oxide
60 oz Water

→ Mfg by Colorizer Associates
Chicago Ill.
. Mat is Combustible

P Bank Saddles 24 to 38 Ready
for grout Will Start Tomorrow

---

48 - 35 to 25 Ins Saddles grout

Shoring 9th floor 43
Shaft 2 Drop Plank
above landed on 6

40th - 21-22-23 North 38-39 H
45-46 East 45 - - 8-9-10 South

5-27-20

Core Board & Shet Rock
#5 Shaft Sealed F-1/2
Left 5 # 48 - Core only
from 39 Down

Layout 3 - 41
Inst Bott Track 35 - 5
Inst Studs 32
Top Track 6 - 5
Plank - Sheetrock 29 - 30 - 32
Plank Shaft Shaft 5-48 - 36 to 40
Pick up framing 31
Total 57 men

5-26-70 cloudy

Check Distance bet Steel Studs 16" o/c

Protection of Cars # 34 - 42 Cap
Working on 35 - 43 - 5

Spraying Cafes on 6th floor
Not spraying on 10 fl
ran out of material

Sam - Mock up of Toilet 10 fl.

Van Shaft #6 Jump to 6 9 floor
Pour to June 10 (54)

Checked with Surveyors - saddle
running 3/16 of dimension 1 of 3/8

Protection on part of Shaft #5 - latches on doors -

5-26-70

Removing Tarps where DeBrava is completed
40 floor El Bucks a jump
Temp Protection Shaft 42

Layout 40-41
Top Butt Track 32-33-34-35-36-37-38-39 5-48
Set Plank 32-33-34-35-5-48
Protect 32 to 39 - 5 & 48 - 30
Set Studs 31-32
Butt Track 33
Plumb Top Track - 6
Framing Stairs & Bucks 6
Set Plank & Sheet 31-30-29
Pick up Jamming 30-31 (54)

35-43 Set Frame
24 floor 48 Fl - 5 men / foreman

8 AM - 4:30 pm 4:30 Worked to 3:30 Am
10:15 PM

5-28 Fair

Layout 3 third - 41
Plank & Sheet 39 to 41 - 33 - 32
31 30
Bolt track - 36
Studs 33
Joining Elm Backs - 32 -
Top track - 6 - 5

Maint - Loose Wire
Doors etc
Sunday Work 7 hours
Car 6 - 7 do All
Shafts -

Spraying overcoat 11 H

Shaft 7 - Tower B

5-29-70 Friday
Fair Clear

Protection 45 floor 2 shafts
Elev 51-52 - 2 men

75 ft No Tacks on get

Butler
Stair chopped - Concrete
left on landing &
stair
Utley -

AWR Buck 5th floor
No Steel in Contract
AKR-4th

[redacted]

Friday
5-29-70
(110)

Layout 2-7-41-48
Bolt Track 36-37
Forming Elev Doors shafts 36-37 45-46-47
Inst Bolt & tip Track 5-6
Forming Stairs 5-6
Inst Studs 35
Plank & Sheet 31-33-34
Plank 32
Curbs forming 32
Protection 8 men

54 men

Meeting ~~Thursday~~ Tuesday PM
Elev Con 36

Sunday - 5-31-70
Fair

Retired - Replaced where necessary Wire Protection on car #7 from 60 fl to Lobby
4 Cpt 1 [illegible] 1 [illegible]

Checked All Work accomplished by Star Creek [illegible] up to date from 40 fl to 10 fl Jackson

---

Monday 6-1-70 Clean
Fair

10 fl Temple Toilet
All ½ Shut Rock up on
N E - W Walls - & ½"
W.R. Shut Rock up on East Wall

Layout 2 to 6 Inc
Forming & Sheet - Bottom Temple 10 fl
Inst Studs 17-18 Mach Room
Inst Studs 6 - 32-33-34
Bott & Top Track 5
Hang & Bucks - 5
Bott Track 4-5
Top Track - 4
Block & Sheet 31-32-33-34
Pick up forming 33
Block - Sheet Machine Room 17
55 men

Tuesday - June 2 - Fair

110 down the PM - Car #36
28 to 33

9:30 PM - Hunting Malins

---

2 Core Boards with H feet
Top & Bott "J" - with
Hoffle fastened 1 H feet
200 lb then 250 lb
for load test only
Fucarelli notified Morete
they don't know Who else
was invited - (USG)

Layout 2 to 6 Inc
Spiderwork Toilet - 10
Plank & Sheet 17-31-32-33
Deck cap forming 33-34
Studs 33-34-35-36
Plank 34-35
Stair - Bucks - 4
Bolt track top track 4 . 55 Men
Overtime Shaft #36 - 28 to 33 Inc
19 Cpts - 2 Foremen
- Bomb Threat -

Release 9th floor Shafts

Start to Plank way
5th floor as per J Fucarelli.

---

113 Dr Brown Inc
Req as yet have to
Wait for Dr Brown to get b
for FLA

Sample for Test Set up on
10 floor S.W Corridor

Star Will start Weld Any
On 10 fl to complete ~~by~~
all Walls -

Started to Install Damper
Units ... for
SE Elev

Wednesday June 3 · 1928
Fair

Test Panel
200 lb Test
Deflection A 1/4 B 5/16
700 lb Test
Deflection A 1 1/16 B 1 5/32

Distortion 1/8" 1/16"
after Load Released

Joist Studs 36 -
Block 35 - 34 -
Block Sheet 33 - 32 - 17
Putting forms 34
Bolts 10
Studs Block 10
Layout 48
Forming Elect Closet -
Belt Track 38
Forming Stairs 3
Top Belt Track 3 - 4 - 10
58 men

Soaking Soap Piping Test

All Drilling to be Color Spray or Removed. Dr Bonn

Thurs June 4 - 1970

Holtzmueller - Adler Nelson Clark
Stairs remove debris -
Bert Weintraub } overspray ducting
Debona } or remove
Bert Weintraub Electrical closets
4" strips

Layout 48
Temple Toilet - 10 fl
Set Bucks 10
Set Plank - Sheet - 10 - 17 - 18 32-33-34 35
Set Studs - 17 - 18 - 36 - 37
Build up forms 34
Bolt track 38-39-10
forms Stairs & Bucks . 3 60 men

Shaft #5 Protection 8/30/11 -
5 - 1 Foreman (7)
1 Shop Steward
Signing Sheet for
Stan Bunch 6-19-70

Shaft #5 - Protection -

Proceeding 10 fl to complete
Core Board of ~~Sheet Rock~~
Also Sheet Rock on
Electrical Closet as Sample
on 32 floor - Is this
Approved? -

Overcoat spray is only
on Cafco D "old" ??? Advise -
ask De Bona -

Friday June 5 1970

Cloudy Rain

4 Men Protection on Car #5

113 - Spraying 43 fl.
New Cap 32 fl top 6 ^.
& fin 36 up

Spoke to Fred Canardo Re closing 10 floor - Fred stated ~~that~~ Gussman & Weinstein were going to take De Bono bodily out of office to 10th floor to settle this. Joe Buck slips to Joe Lee to leave board out & he said Bell Stat - I'm ~~good~~ going to do what Bert Weinstein told me -

Blackie Layout Man Stan Reich left today after Job Albany

Warren Pete 10th floor
8:30 AM OK

Notified Warren Re finishing Trades inside Core & 4" Strips

Stan Cabbering 10 floor - on Bert Weinstein orders. De Bono Must Patch Voids - told Frank Holtzmark on floor he state De Bono's foreman will do nothing until they ~~have~~ receive orders from office

Car #5 Overtime Protection
5 Opt. 1 Foreman

Layout - 47 - 49 - Plank Sheet 34-35-33 10-18
Dept Stats 37-6 Belt Track - 39
Top Track - 40

59 Men

Monday — 6-8- Lou

113 - DiBova Spraying 10 floor
Capco filling Voids - & Spraying
Nickels Overcoat -
Also picking up PT Cells

Layout 49
Mockups Toilet 10
Set Bucks 10
Batt Track 10
Set Stairs 10-11-12-36-38
Block Off Shaft 34-35-18-10-11
Picking Forms 36
Set Block 36
Forming Stairs & Bucks - 36
Top Track 40

60 Men

Start Mon - Motor Room
& Generator Room Cab
51-52
43-44 Spray Bar Joists

Tuesday June 9- 1970

Spraying 43-~~44~~ Saw

Jilly lift -

Patching & Spraying one coat

Layout 49
Top Batt Rock - 40 - 45 - 12
Steel 5 - 11 - 38
Block & Sheet - 34 - 35 - 36
total 59 men

If Pipe does not Permit 2 Layers of Sheet Rock use 1 layer of W.R. then up with Reg S R and turn down as far as we can go with W R

(36) - 37 - 38 (9 floor)

11 up 19   24 men
3:30 to 8:30   2 ~~2~~ Sal ?   26 total

6-10-70- Wed.
Fan

Check Shaft #6 Jump from
54N 69- Protected ? -

	N	E	S	W	Doors
69					
68					
67		X			
66					
65	X	X	X		
64					
63		X	X		
62	X	X	X	X	
61	X	X	X	X	
60	X	X	X	X	
59		X	X	X	
58	X	X	X	X	
57	X	X	X	X	
56	X	X	X	X	
55	X	X	X	X	

54 Ready to go down
Elevator Buck B by Sect 51
Bank A

Protected NE Elect Closet
High as can go
Stair 41 up

Cut Down doors 48 fl
6 & 7 Begin across top

Wall Studs ~~typ~~ 9'-0 - Short 1'6"
on unit side on Bowl side 2'6"
~~[illegible]~~ 2 Metal Studs on unit side
opposite 6 Reg

one Horz Stud

Don Buck - Must use 1/2" Sheet
Rock in order to recess 3/8 Tele
System 7/8" BB to Stud Pad
West Stair 2nd Bathroom unsupported
Caulking tag & Bolts also East
11 fl Ele Lobby A Bank 2nd Bathroom
Sheet Rock Cut Short in Stairwells

6-10 Conti

Layout 49
Pullout C & Sheetrock 37-36-35=140
Build up forming 36-37
Inst Studs 36-38-5
forming Stairs 39
Top Track 45
Top Track 2½" 13-11
Sheetrock Toilet 11
Elev Lobby- 11 58 men

6-11-70 Sam Thursday

113 - Spraying Banjons 44
clean floor 43
11 fl spraying around
Columns closed by Star -
10 fl - 1008 - 1007 - 1006 1004
1003 1002 1001
11 fl 501 - 502 - 503 504 505
506 507 - 508 - 1008 1007
1006 1004 1003 1002 1001

6-11-70

11 - Star Steel closing up
now 11 floor -
Safety Hats -
Plank & Sheet Rock 37-36
Picking Jimmy 37-38-10-11
Set Stairs 37-39-5
Set Bucks - 11-12
2½" Track - 11
Ironing Stairs 40
Top Track - 46 60 men

Friday 6-12-70
Fair

118 - Star closing walls on
10-11 - Not cleaning inside
Wood Planks - C channels &
other Debris on Beam flanges
Star laying off 17 men today
Star received Speed Letter from
Tishman re damage to Toilet
Depis by Star - USG Joint Compound
Star to Write letter to Tishman
Re changing Epoxy to ~~[illegible]~~ Joint Compound
Pitts changes to go to slab
now on 10 & 11 they are going
to go from top of 9'0 to slab -
Layout - 46 47-48-49 Pullup
Set/Plank 38
Pull up forming 38-39
Plank Steel - 37-36
Set Hook 39
Top Bolt Track - 43-44
Top Track 46
Toilets - 10 flr
2½" Studs - 12   Total 60 men
71



Bench Mark ½" off bot (2)
51 fl - Bar K A - 18 Column

51-52 - Protection of Bay 52-5
Complete doors - 5 days

Spraying Caps Bar Joint 44
Patch - 12 -
Spray [illegible] 12
17 fl East ~~[illegible]~~ Elev - for
stilling through Core Beam
up 5'4 above floor - Steam
Burnt off.

Star Ceil Shorty Brothers into 1 Sp
[illegible] Spreader Wires - Sound Elev -
Cut

6-15-70 Monday
Sam

Check All Elev opening Block A
D Zone 1

Pete VAGNINI

Vert Shafts 39
Top Track 47
Block 38
Block & Sheet 37
Bott Track 47
Vert Bucks 13
Jacket 12

(44)

Punch list Kemper Ins
Putting Protection

113 Spraying 6th floor level
44 Box Joists
12 Patching & cement

6-16-70 Tuesday

Door Bucks Received 118 Frames
Ticket # F-08655 900 clip flags
6-15-70 Ticket date -

Layout 50
Top Track 45-47-
Int Studs 39
Block 39
Block & Sheetrock 38-37-11
Int Bucks 14
Toilets - 12
Elev Lobby 12-13

45 Men

1135
Patching 12
Spraying cement 12
Bar Joists 44

Elevator Bucks - Local -
as per George Hughes

404 Mfg
387 on Job
17 to be shipped
to be used - Zone 1 - A B C D } 1 man
Zone 2 - A-56 } A
Zone 1 - A Block 50
Zone 1 B Block 10

Wednesday 6-17-70

Top Track 48
Inst Studs 39
Layout 58
Inst Block 39
Block & Sheetrock 38-12
Foaming Toilet 11 & Planking - (43 men)
Elev Lobby Sheetrock - 13

Protection - (29) + 1 31

113

44-45 Banjack
6 PM
11-13 Protection
Spraying 12 overspray

6-18-70 Rain
- Thursday - Fair

Layout 51-50
Inst Studs 4
Inst Block -
Inst Block & Sheet 5-12
Top Track 48
Top Butt Track 5
Elev Lobby - 14
Pick up framing 14 - 2 & 2½" Stud
Inst Bucks Toilets 13
Framing Toilet 11
Sheet Rock Core - 2½ & 2" 10
Taping 11-12 toilets 44

Pointel — 30

A-AB214

Starting Tile Walls - 10 floor
West Mens Toilet

~~Start~~ Starting to finish Walls
Condor - Etc -

Taping 12 floor - Spackling
Toilets

Started Core & Sheet Rock 5 fl

DeBona Same as yesterday

Friday June 19 -
Fair

Sample Toilet Tile Womens #2 10 floor -
21 Door Buck's 10 floor
21 " " Even floors
22 " odd floors - App -

Layout 51
Top track 48
Top Bott Track Elev Shaft 5
Insul Studs 4-5
Plank & Sheetrock 5-13
Sheetrock - Core 2 1/2 Studs 10
Framing Toilet 11
Insul Bucks 14
Framing 2 1/2" Walls 14
Sheetrock Elev Lobby & Stairs 14
1 Taper - 12-14 (46)

Protection ~~30~~ 29

110

& Corner Bead # A-AB312

PVA - Plaster -
Sealer.

---

113 - Page 80 - Dampening
coats. Par 3 -

Sunday June 21 - 192[illegible]
Fair
Star Circle - 160 -
6 Men 1 Foreman
1 Shop Steward

Started Job 9:45 for
Car from Otis

4 PM

#6

Worked Left 8 to 5:30 Rainy

June 22 - Monday
~~Rain~~ Cloudy

44 ft Zone 2 - Bank
A - M - Elm Beds
also protect from being
removed by ... on cars
51-52? -

Elect Closet - 40 to 18 ...
18 ft - 3 Plants ...
why - ... 9 to 40
N.E. ...

Malone & Debbie in
cool Area - 44-45-46 ...
cannot unload Trucks!

2 Men Post Mori
Cleaned floor ...
Ready for Inspecti...

Electric Closets North
... must be completed
Scaffold - Approved?
Bring ... on
Need more Planking -

Layout 51-52
Top Track 49
... 4
Plank & Sheetrock - 5
Sheetrock 2½" - 10
Taper - 13-14
Top - Bott Track 4
Joining Track - 11

45 Men - Protection 3...

June 23 - Tuesday

Fair -

Layout 52
Top track 49
Top & Bullet Track —
Blank & Sheetrock. 5
Taper 13
Framing Toilets 13-11-12
Elevator Lobby 16-17
Build up framing - 6-4
Insul Studs - 3-4-
Sheetrock Toilets
Insul Backs - 15

30 Prod - 15 non Prod - 45 total
Restrictors - 27 - 3 non Prod - 30 total

115
6 th floor -
15-16 Patching

8AM - 10:30 PM

14 hrs -

3 [illegible]
1 Form
1 [illegible]

(D)

8:30
12:30
4 hrs

Wednesday
6-24-70 Fair

Layout 53
Top Track 50
Joist Studs 3-4
Pick up forming 6-5
Block & Sheetrock 4-5
Sheetrock Core 2½" - 10
Sheetrock Toilet 10-12-13
Joist Beds 15
Sheetrock Elev Lobby - 17-18

47 men Prod 30 Protection

---

113 -
Patching 17-18
Overspray 13
~~Coso~~
Mark 2 - 6

Thursday. June 25 1978

Jan

Layout 53-54
Top track 50
Top & Bott Track
Joist Studs 3
Plank & Sheetrock 5-4
Sheetrock 2½" Studs - 15
Sheetrock Toilets 10-13
Joist Bucks 16
Sheetrock Elev Lobby 18
Pick up forming 6
Sheetrock Core Walls 10
forming Toilets 12
33 Production · 16 Non Production 49
27 Protection 3 overhead 30

Double Studs at doors ?
Dispenser on toilet Line up
Caulk type of Sheetrock to ceiling etc
Straight Edge on walls toilets

56 floor Plates. NW - Elev
26 Clips

55 flr Comp - All clips

45 Bar Joists
6 · Overspray
13 Overspray
19-20 Patching

113

53 Bucks · Below grade
All today

June 26 - Sunday
Rain

Check Book - ~~15~~ 11 - 3 Stair
Damaged Page 70 Row 32

Layout 54
Tie Track 58
Blanket Sheetrock 4
Joint Study 4-3
Pickup Forming 5-6-15
Sheetrock 2 1/2" 10
Forming Toilets 14
Joint Bolts - 16
Sheet Elev Lobby - 18-19

49 Men 30 Arbeiter

A-AB-212-H STU
Open Gypsum Page 94 Line E
Steel Plate - cut air Stop

~~[illegible]~~
Overspray - 6
Patching 21-22

Stair Circle 3.'30 turf
Platform South Exit
#7 Car - on floors 48-49
8AM - 10:30PM 14 hours.

June 29 - Monday
Fair

Tower A - Elev - Temp 61 & 62
Shaft
7th floor 69-74

Laquet 9-54
Top Track 51
Bott Track - 45
Dust Stads 4-3
Plank Sheetrock 4
Sheetrock 2½' 11
Plank Sheet 12
[illegible] Toilets 14
Dust Bucks 16-17
Sheetrock Elev Lobby 19

52 Men 30 Protection

113 - 45 Bar Joints
Stripped - Patching
Complain that some one is running Winders & Cutting Rope on Taps - He is getting too many [illegible] -
Intg
Loading 48 floor - Con Boom

Ster - 3' 30 feet
Shaft - 36 · 37 - 38
19 feet 23 ft Inc

11 Men -

Tuesday - 6-30-20
Fair

Layout - 9- ~~8~~
Top Track 51
Bott Track 3
Int Studs 6
Plyw'd Sheetrock - ~~2~~-4-5-
Sheetrock 2 1/2" Studs 10
framing Toilets 13
Core Shaft Walls - 13-10
~~52 Men 30 Production~~
Sheetrock Plastr Toilets 14
Pick up Core forming 16
Int Bucks - 17
52 Men - 30 Production

112
Spraying Bar Joist - 45
Patching — —
Overspray - - 13

Wednesday 7-1-70 fair
WTOE [illegible] [illegible]
Floor - 1 - 2 3
16 out out ✓ outside
15 out out ✓ inside
14 out out inside
13 out out ✓ inside
12 out out ✓ inside
11 out out ✓ In
10 ✓ out ✓ out ✓ inside arc
9 ✓ out ✓ out ✓ [illegible] arc
8
Sargent - 7-9
Dank [illegible] Shattuck 4-5-6-14
Top Track - 51-52-2-3
Asst Stacks 3-16
Asst Bucks - 17
Asst Shattuck - 10
total 51 men - Board -
30 men Post

113
Barfoots 45
onedying 14 13
3rd flo 6

1-30-70 10-16 on floors
AD 38 to 47 -
Soap Dispenser
10 fl outside
11 fl. Inside Stall

Trellis
70 jars - F 08738
77 jars F 08824
144 - AK - Ad

Thursday - 7-2-70

Rain

Layout 55

Blank & Sheetrock 4-

Inst Studs 9-3-6-3

Inst Bucks

Inst Sheetrock 2 1/2 Studs - 10-11-14-15

Top Track 5 2-3-9

Bott Track 3-9

Framing Toilets

Framing Slen Shafts 4-3-[illegible]

50 men Prod - 30 Protection

Bar Joints 45

Spray - 14

Patching - 25

Friday 7-3-70
Fair

Layout 55
Top Track 52-53-9
Bent Track 9
Blank & Sheetrock 2-3-4
Inst Studs 9
Inst Bucks
Inst Sheetrock 2½ - 11-14
Jamey Elev Shafts 41
Inst Block - 3
42 Men Production
14 Men Protection

113 - No Work Today

Monday
July 6-   Fair

Emergency 1411   113

Layout √6
Top Track √3
Top Butt Track 42-8-
Shut Heads 8-7-17
Block & Heeltack 2-3-15
Heeltack 2½" Heels - 11-12

47 Men - Paid
80 Men Out

Craft 108 - Court Hartz 294 lbs
2 Men / Super

110- 6
113- 1
108- 1

Elm #7 Jump to 74 - July 10-
Elm 61-62 - Out on or before July 3
CBank-

July 7- Tuesday
Fair

High Realty- Core Marble Ready?
Check A Block } Marble Ready?
B Block }
Line up Napkin & Soap Disp
Inc- Re. Lobby Core Board.

Craft on 294 Label- Cont
Shorty 2 men 1 Laper

110 6
113 1
108 - 1

Occupancy - 14

Layout	56
Top track	53
Top Bott Track	43 -7-3
Just Studs	7-8
Block - Sheetrock	3-5-9-15-
Sheetrock 2 1/2"	12-14
Just Beads	18
Taping	10

49 men Production 3# 19
30 men Protection

July 8 - Wed Fair

(112)

Layout 57
Top Track 53-54
Studs 3 - 7
Blank-Sheetrock 3-5-9
Sheetrock 2 1/2" . 12 - 15 - 22 - 24
Taping-Spackling 1.0 - 11
Bucks 18 ft.

51 Men Production
31 Men Protection

108 Shorty - 2 Men - 1 Supt

143 Ominspray 14 ft

July - 9 - Thurs. Fair

15 Ominspray (113)

Layout 57 (110)
Top Plate & Track 54
Joist Studs 3 - 6
Top-Bott Track 7 - 8
Blank Sheetrock 3 - 5 - 9
Blank 6
Sheetrock 2 1/2" 11
Taping - Spackling 11
Toilets 15 - 16 - 12
Bucks 18

52 Men Production
30 Men Protection

Shorty on 294 Level 108
2 Men - 1 Super

7-10-70 Friday - Rain

Car # Box K A - Zone 2 -
Operator on Job - 9:20 Am

Layout 57-58
Top Plate & Track 5-4
Jnt Studs 7-8
Blank & Sheet 9-16
Sheetrock 2½" - 11-12
Framing Toilet 15
Bucks - 18

50 Men Reed
30 Men Protest

110

Shorty - 284 - 2 Men 1 Helper 108

Oneway - 14
Patching -

113

High Rely - Core Marble Ready ?
Check - Bank A } Marble Ready ?
Bank B }
Fire up Nipples & Soap Disp - 10 fl
Stair - Lobby Core Board ?

Short - clips - where
one not Welded
4 Hole -

3rd floor Stair 2 -

Bill Mueller

106.38' =
103.7' =
2.68' =

7-12-70
Sunday [illegible]

6 Cpt
1 Hept
1 S.St.

Jumping Cart
-7 to 74 floor

[illegible] - 7 AM - 5:30 PM -
[illegible] 8 AM - 5:30 PM

~~||||~~ ||||

7-13-70 Monday [illegible]

Protection - 28
Restoration - 49

Layout 58
Top Plate & Track 55 - 7-8
Inst Stairs 7-8
Plank & Sheetrock 6
2½" - Sheetrock 11-12-18
Forming Toilets 15
Inst Beads 18

108 Layout checking
[illegible]
John [illegible]

113 - Mr [illegible]

July - 14 - 1970
Tuesday - Fair

Layout 59-
Top Plate & Track 55-56
Bott Track
Plank & Sheetrock 6-8-16
Sheetrock 2 1/2" 11-13-15-16
Framing Toilets 13
Int Bucks 19
Top & Batt Track 7-8
Production 16 Non Prod 34 Prod 50 Men
Production 3 Non Prod 25 Prod = 28 Men
Int Studs 7-8-41

Why start Here 24" O.C

113 - No Work on This Contract

118 - Drilling Holes in Balcony for Bolt Holes for Railing Posts
2 men
1 Layer

Wednesday July 15 1970
cloudy -

Star Circle -

Laygent - 2
Top Slate & Track 5 6 - 2
Inst Studs 41 - 42 - 8
Top Batt Track 8
Sheetrock 11
Sheetrock 24½ - 13 - 16 - 19
Block & Sheetrock 17 - 18 - 8
Inst Block 7

80 Men
28 Rest

Roads Eng
Al Cosmos 10th Below 310
Bob Wright 3rd NE Plaza
McGrath 3rd Canton House
Dave Brown 10th Tower above 310

Bricklayers Craft Shanty Block 4
Glass Stone Circle Saws -
Craft 4 Men
1 Foreman

Shaft #5 - Sat -
Shaft #7 Sun -

July 16 fair
Thurs.

Layout 2
Top Plate & Track
Inst Studs 42-43-44-9
Top & Bott track 9-7-2
Sheetrock 11
Sheetrock 2½-11-13-17-19
Plank & Sheetrock 6-7-8
Inst Plank
Forming Toilets 16
Inst Bucks 1.9
Perf 50
Dust 28

8 fl - Wet Elev 29-30 A-B Bank
8 fl Wet Elev 29-30 Top. Mont
Concrete NG - Butch Plate here

Questioning - Shaft 1-2-3-4
3:30 - 9:30
20 ext 1 tape 39 to 44 Done
Machine Room 3-4 - under Cont
310 OK Temp door
44 Temp doors

113
Patching no
Overspray 14-15-16
Spray Bar Joists no

108 ~~Drilling Balcony~~

Drilling & fastening
Install on 264 level -
Observation Platform

Frank Turco 14 Hitch fixes - 20 Head
Pete ~~Vaag~~ Vagnini - 4 Hitch fix
fell over debris on floor - Peter Turco
to catch & both fell & got up on
4 Sections - (39 floor) Stairs

Fri - 7-17-70

Fair

Protection (30)-
Production 48

Layout - 59
Top Plate & Track 2-7-8
Inst Studs 2-7-8
??? & Bolt Track 2-7-8
Sheetrock 11
Sheetrock 2½" 13
Plank & Sheetrock 40-41-42-78
~~Plank~~ I 17 9
forming Toilet 16-17
Inst Bucks 19
forming Elev Shafts - 44-45

254 Spoke to Zeis Nothing ??? Shop ??? around Plant. Logs & office scheduled to return Monday. 7-20-70

overtime set Project Protection shaft #5 - Concrete #50

113 - Tower B - 7th fl.
Patching -
Overspray 16
Bar Joists

110 - overtime 3:30 - 9 PM 1 hr
Shaft-3 #4 37 to 44 dec. 12 ?? / 14 ??
Machine Room. Bank A - 17 floor

108 -
Testing on observation 284
Roof Str. included Balcony

Fri 7-18-70 3 Am.
North West Corner - at crane
69 Planks damaged - 3x12x20
77 18
76 3
75 10
72 3
71 23
69 10
67

Sat 7-18-70
Sow

Rickie & Vreeland
Concrete

Stan Working outside of shaft #50 - Fred Concrete stop them - They were jumping Concrete about 2 floor & men were working in Basement - Stones were falling down & they complained - Stan changed over to shaft #5 to complete.

(50)

Worked on 5 ~~F~~

7 Cpt
1 Supt } - 8 to 3:30

daily 8-4:30 hrs

Sun 7-19-70

Worked on 6-7- Protection

7 Cpt
1 Supt } - 8 to

7 Am - 4 30 hrs

Fire Engine Called over
11:45 AM 1st Batt.
6 - Pumper
10 - 1 Truck & ladder
71 floor - fire Exit set up Bracket

7-20-70 Monday
Fair

110

Production 31 men
Reproduction 47
Layout 61
~~Top Plate & Handle~~
Inst Hood 2
Top & Bott Track 2
Sheetrock 11
Sheetrock 2½" 19
Plank & Sheetrock 2-7-9-17-18
forming Tablets 13-17
~~Inst Brack~~
forming ~~Elev Shafts~~

Broken unit Trestle on 10 fl
Stabr - 5 Bays Screw.

---

17 fl. Nervous door should be
20" is 16" - Plumber

106
4 floors of Terrastone 11-12-13-14
Bldg Port Morris - Delivered
Marble for Elev Bank A Ready
A Start Inst
258 Cutter starting on Mail Chute

408
Croft on Balcony Tower A
Drilling for Railing

---

113 - Marie & De Bure A
~~Patching~~
Surveying 1½
~~Bar Joints~~
7

Tuesday July 21
Sai

Layout 61-7
~~Top Plate & Track~~
Set Studs - 2
Top & Bott Track 7-8
Sheetrock 9
Sheetrock 2½" 13-18
Block & Sheetrock 8-2
Framing Toilets 13-17

Men - 45 - Production
31 Protection

108 Craft
Drilling Holes Balcony Tower
for Railings 2 men 1 day

106 Atlas Port Morris Stone ✓

10ff. Mens Room Tile Walls
109 App 7 day for Walls - per floor
5 day for floor = 1 Team

Tronatonion 11 floor Bank A

113 - Working A Tower

Wednesday July 22 –
Fair

Stay Crew 11B
Protection - 31 -
Production - 46 -
Shaft #4 Wire hung on East Elev
Rec Elevator @ 9:30 AM. Men
Waiting 1 1/2 hours working.

Layout 7
Top & Bolt Plate 7-2-8
Joist Heads 7-2
~~Sheetrock~~
Sheetrock 2 1/2" 17
Plank & Sheetrock 18-9-8-2
Toilets - 13

Craft Art. Drilling Balcony for
Rails 2 Men
Drillers

Cutter Joist Mail Chute
294 Level to 310 Level.
2 Men

Atlas Port Mains 106

Travertine - 11 Floor Back P.
4 Men

Toilets - 2. 1 P.H Mens
Jutting Walls. 109

11B De Berry
Nothing

Thursday 7-23-70 Lou

110

Protection 31 - 3 [illegible] 28 [illegible]
Production 47 18 [illegible] 29 [illegible]

Layout 1-61
[illegible] Bolt [illegible] 7-8-3
Sheetrock
[illegible] Sheetrock - 18-8-2
Sheetrock 2½" 13-14
[illegible] Toilets 13-14
[illegible] 7-2
[illegible] 12
[illegible] 2½" Stud 20
[illegible] 20

8
2
3
4

[illegible]-Pete-Al-[illegible]-

(258)
Cutler [illegible] of Mail
Chute 310 [illegible] 294
2 men ✓

(108)
Craft [illegible] Drilling 1 Holes
Balcony for Railings ✓
2 men 1 [illegible]

[illegible] Port [illegible] 4 men
(106) [illegible] on 12 floor ✓
Elev Bank A.

109 Bathroom 18 floor Tile
walls 2 men

De Bona (113)
Nothing

7-24-70 Friday
Fair

Layout 61-7-8
~~Top & Bott Track~~
Sheetrock 2
Sheetrock & Block 7-8-20
Sheetrock 2 1/2" 14
~~Forming Trucks~~
Int Studs 8-2
Tape & Spackle 13
Forming 2 1/2" Studs - 20
Int Bucks 20
Top Plate top Bott Track 4-5-7
Block 18-20

Production 44
Protection 31

(258)
Cutler - Int 294 A
310 Mail Chute
2 man

Craft Art (108)
Drilling Holes Balcony
for Railing
2 man 1 Supt

Atlas Port Morris 106
Insulation 12 floor A
BANK A - 4 man

Tile Walls - 10 floor
Toilet
109 2 man

Mountain Bonne [?] - 113
Olumpney [?] 17

Monday Cloudy Fair
7-27-70

Layout Tell Boards 40 to 61 Inc
T&E Base Track 6-7-8-7-9
Sheetrock 20
Sheetrock 2½" 14-20
Block & Sheetrock 2-3
Inst Studs 2-3-7-8
Tape & Spackle 13-14
Loaning 2½" Studs
Inst. Bucks
Inst Block - 7-18

Producers 41 men
Protection 31 men

Distribution of Copy of Recording by Uko - Stair Rep 166 - (R)

Circuits Ford

---

108 Craft Art
No work on this contract

Atlas Port Morris
106 Transitori (4)
13 floor

---

109 Tile DL
No floor 2 men
Homes Foster

---

113 Main & Debris -
Barjons 46
overhead 16

258- Cutler
Inst Chute 294 level - 310 level
2 men

7-28-70 Tuesday
Fair

Layout 6 2
Top & Bott Track 9-7
Sheetrock 20-21
Sheetrock 2½"
Plank & Sheetrock - 19 - 4-5-6-2
Inst Studs 7-8
Tape & Spackle 0
Flooring 2½" Studs - 20-18-14
Inst Backs 20-7
Inst Plank 0
Plank 7

Production 42 -
Protection 31 -

Protection Floorstairs

#6 Jemb - to 80 - 8-7-70

108 Craft Art
No Work Today

106 Atlas Port Morris Transition
13 floor Bank A - A
4 men

109 Atlas - Tile
16 floor Toilet - Trading A
2 men

113 Main & DeBow
Bar Joists - 46
Ordinary. 17

258 Cutler Mail Chute
2 Mr 320/290

7-28-70 Wed

(110) Ston Fovi

Layout 62-63

Order Bolt track 9-7-1-9

~~Sheetrock~~

Sheetrock 2½" 14

Plank & Sheetrock 21-2-7

Insul Studs 7-8

~~Tape & Spackle~~

Framing 2½" Studs - 14

~~Insul Batts~~

~~Insul Blankets~~

Jigging Toilets 18-14

Production 44

Protection 31

Circle Arc 3 Men

-105- Bath, 1 foreman

Hung Ceiling Corridor -

Bedroom - Elev Lobby

Who to go to for Certificate Welders certificates for Craft Art (Oxygen NYC License)



Caulking Case Walls at Shaft - 175

---

108 Craft Art

No Work Today -

---

106 Atlas Travertine

14 4 Min

---

109 Atlas Tile

11 2 Men

---

113 Marco & De Bona

Bar joists 46

Ordering - 17

---

258 Center

2 Men Best 310 / 2nd floor

July 30 1970
Thursday - Fair

Layout 1-63
~~Bed Track~~ 20-9-8
~~Sheetrock~~ - 0
Sheetrock 2½" 15-18
Plank ~~&~~ Sheetrock 19-7
Int Studs 9-7
Framing Toilets 15-18
~~Framing 2"to 4" Studs~~ - 0
~~Tape & Spackle~~ 0
~~Block~~ - 0
~~Int Studs~~ - 0
Elev Lobby 21-22

Production 43
Probation 31 74

108 Craft Art
Mellonk

106 Atlas Port - Tramontin
14-15 (4)

109 Atlas Port Tile
11 (2)

113 Marine Deli
Spraying Bonfaits 46
overspray 17

258 Cutler Mail
310 to 2nd = 3rd 2 men

115 Arch Arc 10 floor
3 - 5/8 Nail

Friday
7-31-70 Fair

Layout 63
Top Bolt Track 310-8
~~Sheetrock~~ — 0
Sheetrock 2½" - 22
Plaster & Sheetrock 7
Ins Studs 7-8-9
Forming Toilets 18-19
Forming 2½" Studs - 15-18-19
Tape & Sparkle 14
Plaster — 0
Ins Backs 21
El Lobby 22

43 Prod
31 Prot
74-

108 Craft Art
Ins

106 Atlas Transition
15 - (4)

109 Atlas Tile
11 fl. (2)

113 Main & Osborn
Bar Joints 46
Openings 18

258 Cutler
2 to 3rd - (2)

115 Teach Ace (3)
10 floor Ducts in toilet
mens rm low -

Sat Aug 1. 70
Clear [illegible]

4400

[illegible] [illegible]

Tieing [illegible] 50 fl. [illegible] -
Spacing [illegible] 40
[illegible] [illegible]
56 [illegible]

1 Joseph [illegible] [illegible] from
floor Aug 8 [illegible]

45 Men - Collyer

Drilling for Castings 60S - 59W
Setting Castings 56 - 57
Welding Steel [illegible] [illegible] 55
" " " Joints 54
Pick up Missed Welding of [illegible] 53
Welding [illegible] [illegible] [illegible]

Monday Aug 3-70
Office Fair
Layout 1-63
Top Batt Track 8-9-310
Sheetrock 2 1/2 15
Closet & Sheetrock 20-7
Joist Studs 21-8-9-1
Forming Toilet 19
Sheetrock Elm Lobby - 22-23
Forming 2 1/2" clad 21
Taping - spackling - 20

8-3-70

108 Craft Office

106 Atlas Transtime (15)
office

109 Atlas Table (11)

113 Main D. Bona
Barfunts (46) Office
occupancy (18)

258 Cutler
office

115 Circle Ave (10) Mail

Moving Drill Mach #60
Indicate RH Side Bucket 41/1

Star Circle 110

Lampert 5th floor B

Top Bolt Track - 59

Forming Elev Bucks - 54

Door Studs - 9

Sheetrock Elev Lobby - 30

Forming 2 1/2 Studs - 23

Bucks Door - 23

Sheetrock & Plank - Lobby - 9

Sheetrock & Plank Toilet 2" - 22

Sheetrock Toilets 2 1/2 - 18

Taping Toilets - 17

Sheetrock Core walls - 11

Production 30 + 16 Lam = 46 total

Protection 33

R 17 - San Munday

108 Craft 2 men - 1 Supt

Drilling & Balancing A Tower

South Elev

106 Atlas Transition 21

21 floor

109 Atlas Tile - 14

113 Main & Newman

No work with Cat

258 Cotter

No work -

Star Cutch 100

Layout 6 ft - B
Top Bolt Truck 61-59-43
Sh Study 9
Plow Shuttle 9-L-11
Sheet & Block Table 22-23
Shedrock Table 2½" 19
Loomy 2½" Stick 23
Ont Bucks 23
Tape Trucks 18

48 men -
33 Men Out

81
4 Loss

85

Tuesday - 8-18-70
Fair

108 - Craft Art
Drilling Balcon 2 1 3

106 Atlas - Terrazzo (21)

109 Atlas Tile (14)

113 Marie DeBiera
2 Men Benjamin 4B

208 Carden
McNoil & Ashley

110

Layout B-6
Top Bolt Track 61
Jnt Studs 35
Block & Sheetrock - 34-35-36
Sheet & Block Tile 23 -
Sheetrock Toilets 2½" 23-19
Forming 2½ Studs
Jnt Beds 23
Tape & Spackle - 18
[illegible]
Forming Elev Beds 62-63
Jnt Block - 31-32

51 Man Total
33 Bolt
4 Frml
88 -

Wed - 8-19-70
Fair

108 Graff AT
3 Man on Balcony
For A - Railings

106 Atlas - Fireproofing
22 fl

109 Atlas Tile
14 fl Toilet

113 Morris De Bern
Bm Joists 48 floor

288 Carter

110 Sta B 3-8 (Layout Comp)

Layout B — ? 7-8
Top Bolt Track 62
Inst Studs 34-35
Plank of Sheetrock 32 L - 34-35-36
Inst & Plank Toilet 23 -
Sheetrock Toilet 2½ 20
forming 2' 12" Studs -0-
Inst Bucks -0-
Tape & Spackle -0-
forming Elev Bucks 46-63
Inst Plank -0-
Load - 68 fl-

Floor
5 Men
3 Prod
8

Can 5 · 41 Nov OK

Thurs 8-20-70

Lan
108 Craft Art
Layout & Drilling Balcony
Track A North Elev-

106 Atlas Travatine &
23 Harts!

109 Atlas Tile (14/12)
14-12

113 Mario & DeBona 48
47 1 man

258 Cutler 28 fl
Mohawk

Metpar - Part on
10 floor mod
256

110 - Star Clerk

Layout ~~B~~ 68
Top-Bolt Track 6 2-44-45
Inst Studs 44-45
Plank & Sheetrock - 36-37
Plank - Sheetrock Pilots - 23
Sheetrock Pilots 2½ - 20
~~Forming 2½" Studs 0~~
~~Inst Bucks 0~~
Tape - Spackle 30-31-32
~~Forming Elev Bucks 0~~
Inst Plank - L - 11 - 12
Stand,
Sheetrock Elev Lobby - 32

Met 10-16 re Protection of marble tile stored Monday 8-24

(5 Men)

Friday. 8-21-78

Fori

108 Craft Art
2 Men Inst Ceiling & Mullions At Fori

106 Atlas Terrazzo (23)
Inst Terrazzo - 23 fl El. Abv
Fore

109 Atlas Tile (12)
Inst Wall tile 15 fl
Inst Floor Tile 12 fl

113 Marie de Bane (47)
Bar Joists - 47 2 men

258 Ceiling
Fore Nydock Today

256 Metpar - Toilet Part (10)
Fore As Reported 8-20-78

110

Layout 60-
~~Top Butt Leak~~ 63-46-47-42-43
Int Studs 46-47
Block & Sheetrock L-37 $\frac{24}{33}$
~~Block & Sheetrock Toilets~~ 0
Sheetrock Toilets 2½ - 20
Framing 2½ Studs - 21
Int Bucks 23
Tape & Spackle 10-
~~Framing Elev Bucks~~ 0
Int Block 38-12
~~Load~~
~~Sheetrock Elev Lobby~~
Sheetrock - 11

52 Men Prod
33 Protection
4 Hoist

89-

Mon - 8-24-70
Fair

108 Craft Art
Drilling of Balcony for
Rail 2 Men
1 Forem

113 De Bora
Bar Joists 47-59
4 men

110

~~Layout~~ ——— o
Top-Bott Track 60-5657
Inst Studs 5657
Plank & Insulate 38-3334-24
Sheetrock Toilets 2½ 20
Forming 2½ Studs -24
Inst Backs 24
Tape & Spackle 10
Inst Planks L-37-12
Sheetrock 12
Forming Toilets 2½" 24

33 Protection
52 Cord
4 Load

89

Tues- 8-25-20
Lou

108 Craft Art
2 Men 1 Day ∅ Pedan
N-A-Ralen

113 DeBona 47-59

No Work (Tele)

Ceiling Started - (Black Iron)
Tenement Area - Mon
8-24-20 - 2 men

Homosote Board Dusty
Does Not Hold Tape Trying
Staples Through Cloth
Tape & Tape on Marble
OK

110
Star Circle

~~Layout~~ 0
Jnt Block Lobby - 12
Block & Sheetrock 38
Top 2 Batt Track 60-49-50
Jnt Studs 38-39
Sheetrock Elev Lobby 34
Forming Toilets 2 1/2 - 24
Forming 2 1/2" - 24
Bucks Jnt 29
Sheetrock Toilets 21
Taping & Spackling 19
Sheetrock 12

52 Men
33 Jnt
4 Fore
89

Wed - 8-26-70
Fair

108 Craft Art
2 Men 1 Supt Drilling
Balcony Taken A Hall

113 De Bona
Bar Joint 59 2 Men

2:30 Bar

110 -

Layout 66
Joist Plank 12
Plank & Sheetrock 38
Top & Bott Track 39
Joist Studs 39-40
Sheetrock Elev Lobby 35
Framing Toilets 2½ 24-22
Framing 2½ Studs 24-25
Joist Bucks 24-25
Sheetrock Toilets - 24-25 - 21
Taping & Spackling 20
Sheetrock 12
Top Track 60
Framing Elev Shafts 41-42

Production 55
Retention 30
Good - 4
89 -

113 8-27-70 Thurs Jon
Bar Jones
60-47-50.
58

108 - Craft
2 Men
1 Super
Ducting & Balcony
N.C Tower A - for Railings

115
[illegible]
[illegible]
[illegible]
[illegible]

Don Buck K Ave
[illegible] 8-26 Tickets
[illegible] 84 - 66 [illegible]

110 Stor Cuih

Layout 49
Insp Block 13-12
Block of Shutwork 6-39
Top Belt Truck 64
Insp Studs 40
Shutwork Elev Lobby 35
Forming Toilets 2½" 22
Forming 2½" Studs 25
Insp Backs 25
Shutwork Toilets 25-21
~~Taping & Spackling~~ 0
Shutwork 12
Top Track 60
~~Forming Elev Shafts~~ 0

Production 52
Protection 30
Food 4
86

Fri - 8-28-70 Law
113- Main & De Bone
60 - ~~[illegible]~~ - 50
58

108 Craft Supt
2 Men Supt Balcony
Tower A - Drilling 0 -

115 Circle Ceiling
3 Men Insp Block On
C & Pencil Studs 10 flr
Tenant Area

9-2-70 7P-7L-1Sup. (15) 1613
9-3-70 4P-5L 1F (10) 1614

Mat Not Invoiced
for 8-28

Bucks Inst
Mat Loaded
Core Board Inst
Sheet Rock Inst
Protection Stairs
Protection
Toilets Rough Backs
~~[illegible]~~

9-9-70

Booth A Elev - 3 Elev.
by November 4 Others to
Come

1 - Dic - Flashing -
2 - Star - Sealing -
3 - Ditomo - Insulation -
4 - Otto - Paint etc
Everyone clean own garbage if
in doubt Tishman to clarify
& get done -

9-8 3L 2 Ins 3 men 2 Fm 1 Tony 1615 (14)

Wed 9-9-70
Rain

See Star Circle 111 on
Master Sheet. check Telephone Boards -
10-16 Inc -

108 Craft Art - Delivery
Ø Balcony 14 Elev for
Railings - 1 man Off

113 Main & De Boer
Bor Jamb (52) - 53 - 55 - (56)
(51) Comp Margk

115 ~~Ste~~ Circle Ceiling Ok
- No Work today

4-6 - Spray core Column ~~Covers~~ ~~[illegible]~~
PM on 52-53-55-56 4 men.
(161) 3 Laborers - ~~[illegible]~~
1 Mechanic -
3 men Hoisting (7) OK

Thurs. 9-10-70
Cloudy-Rain

Star-110- See Master List

---

113 Main & DeBona
Bonforts 53-55-

Sunday-4-6-
Working Sat-9-12-Sun 9-13 - 113-

108 Craft Art
1 Men Quilty
1 Hyper Balcony A-A

---

115 - Circle Ceiling
[illegible]

53-55 Shafts
Tonight 4:30-7:30
5 ...
4 Lab
5 Machine men
1 Supt

(13)
(1618)

Fri - 9-11-70
Fair

108 Craft Art
Laying out clips for Lobby Panels
332 Elev south 2 Men 1 Hyper

---

113 Main De Bona
Bonforts 53-55

Shafts 40-41-42-43-44-45
53-54-55 & # in Elev Bank A

---

115 Circle Ceiling
Nichols [illegible]

---

110 Star - See List
Mon putting Double Stud at Back & one App 6-8' Away

	Tues 8-4	Wed 8-5	Thurs 8-6	Fri 8-7	Mon 8-10	Tues 8-11	Wed 8-12	Thurs 8-13	Fri 8-14
	Fair	Fair	Fair	Fair		Office - Covered			
Layout	64	64	65	65	66	3 B	×		
Top-Bott Track	310	55-56 L-21	56	57	57	58-57 L	58	58-59	59
Sheetrock 2½	15-16	—	16	16-17			17-18	18	18
Sheetrock	7	—	—	24		L	L-11	11-28	11
Plank-Sheetrock	8 20	8-20 24	8	8 21	8	L-8 21	8-9	L-8 9-24	L-8-9 22
Joint Studs	8 310	8 310	8 L	L	L 8	8-7 L	9	9	9
Tape-Spackle	20-21 22	23-10 15	15-23 11	15-10 TC-11	10	10	24-25 26	16 17	177
Forming 2½ Studs	21	—	—	22	22 20	22			
Forming Toilets	19	19	19	20		20	20-21	21	21
Elev Lobby	23	—	24	24	L 25	26-L	44 27	47-48 49-28	48-49 50-28
Joint Backs	21	—	—	L 22	22	9 22		23	24
Joint Plank	—	L	L	—	L				
Sheetrock Toilets	—	16	21	—	21 17	17	22		18
Forming Elev Shafts									
Handrails Stairs 1-2									
Forming Stairs									
Sheetrock Polyrollers									
Const Stairs Bank A									
Plank & Sheetrock Toilets									

18 19 70

~~Took up~~ with E Boland #1892

×

Car # 6 Jumpers 69 to 80
on 8-9-70 6 Cpt
1 Foreman } 7 hours
1 Steward

Covered by Fred Steinquell
Time out of dept L Approval
of Work alone & Std Hours for Shafts

Mon 8-31	Tues A 9-1	Wed C 9-2	Thurs A 9-3	Fri 9-4	Tues 9-8	Wed Rain 9-9	Thurs Rain 9-10
67	43	43	44	67	67	X	
64-45 41 42	64-46	65 64-44 40 46			65-19 43-44	65	65
22					14	23	
13 12	12	13-12	13	10-13 14	13-14	14-13	13-14
39	39-25-26	39-40-26	39-40-26	40-26	40-13 27	28-41	41
40	40	40	40-41	40-41	42	41	42-41-43
20-21	25-34	X	11-12 Telyh		Eln Lobby	Tele Chors	Tele Chs 16
	25	25	25			24	
22	22	23	23	23	23	24	25
36	37					X	
	25	25	25				
13-40	40-13		13	14-10	14	X 14-13-40	40 14
25-22½	22	22	22	22	23	28	28-24
	44	44	11-12-13	~~30~~		41	41-43
58 men				10	12-13	X	
					43	41-42	41-43
	55 men	57 men	58 men	56 men	62 men	15	16
						Bonk A	Bonk A
						65	65
						OK	

Fri 62 Fair 9-11	Sun Fair 9-13		
65-66	Starlite Jumping Car #7		
14	6 Cpt		
41	1 Left		
43-42	1 Steward		
Tel clank	(8)		
25	8AM 4:30 Till		
14	73086		
24-25			
43	#1797		
16			
Bork CA			
29			
(65)			
31			
96			

Sat - 9-12-70

113 DeBra — Fair

Coal Column	54-	2M - 1L	2
	53-	2M 1L	2
Machine Man	45-	1M 1L	2
2 - 38	44	1M 1L	
1 - 48 1	43	1M 1L	J
2 Super	42	1M 1L	
(169) (26)	41	1M 1L	
	40	1M 1L	
310 Line BorkCA -		2M 2L	
24 Men 2 Super.		9-4 men 8-4 Labor	

(113) Sunday 9-13-70 Fair

Coal Column	54	1M	1L
	53	1	1
Machine Man	52	1	1
1-48	45	1	1
2-38	44	1	1
2 Super	43	0	1
	42	1	1
	41	1	1
310 Line BorkCA -		1	1

9 to 4 - 20 men (22)
8 - 4 Labor 2 Super 16 20

Normal Day 9 1/4 ① 13 1/4 ②

Reg Day 1/6 4 hrs ① 9 1/4 hrs ② 13 1/4 hrs ③

8.5%

Eleven

Date		Comp Time		Total	Exp
Sat 4-11-70		8		8	6.05 ✓
Sat 4-25		9		17	~~6.05~~ ✓
Sat 5-9	-	9		26	6.05 ✓
Sun 5-10		9		35	6.05 ✓
Tues 5-26	16	8	12:10	43	~~7.50~~ 5.00
Wed 5-27	12	4	8:30	47	2.50 ✓
Fri 5-29	16-8? mm	8	4:30	55	6.05 ✓
Sun 5-31	9	9		64	6.05 ✓
Tues 6-2	12	4	8:30	68	2.50 }
Thurs 6-4	15	7	11:30	75	5.00 } OK
Fri 6-5	11	3	7:30	78	2.50 ✓
Tues 6-9	12	8 2 4	8:30	82	2.50 OK ✓
Sun 6-21	9	9		91	6.05 ✓
Tues 6-23	14	6	10:30	97	5.00 ✓
Fri 6-26	14	6	10:30	103 (33)	5.00 ✓
Mon 6-29	12	4	8:30	107	2.50 ✓
Fri 7-3	16-8? 4th July	8 (33)		115 80.90	6.05 ✓
Sun 7-12	7-5:30 10	10		125	8.55 ✓
Thurs 7-16	13	5	9:30	130	2.50 ✓
Fri 7-17	13	5	9:30	135 (28)	2.50 ✓
Sat 7-18		8		143	6.05 ✓
Sun 7-19		9		152 106.55	6.05 ✓
Fri 7-31		1		153	-0-

Date	Hours	Total	Exp
Sat 8-1-162	9 112.60	162 (19)	6.05 ✓
Sat 8-8 7-5:30	10 121.15	172	8.55
Wed 8-12 4:30/5:30	1 (21)	173	-0-
Sat 8-15 7-5:30	10 129.70	183	8.55 ✓
Tues 8-18	Shoes - Safety		10.00
Wed 8-19	1 (139.70)	184	-0-
Wed 9-9 8-6:30	2 hrs	186	2.50
Thurs 9-10 8-6:30	2 hrs	188	2.50
Sat 9-12 8-4:30	8 hrs	(196)	6.05
Sun 9-13 8-4	8 hrs	204	6.05
			17.10

196
143 Pd 9-10-70
53 Bal
8
61

(156.80)

	STATUS 7-31	SAT 8-1	MON 8-3	TUES 8-4	WED 8-5	THURS 8-6	FRI 8-7
Column Covers - Bill	39N		39	40 Pm 39	39 40 Pm	39-40 Pm	39-40
Alum Liners John	14-15 37N		31	33-34	35-34 52	36-35-	36-37 35
Caulking Mario	34S (156)		34 12-2 MEN	34- (23)	35-34 12-2 (137)	36-	36-37
Heads Lruing	36S		37	38-37	37-38	39-38	38-39
Cleaners	29WN 28ES		28-29	29	30	31-30	30-31
Glazing Ed	26ESW 27NES		27	28	28-29	29-28	28-29
Al Core & Bulkhead Marty							
Spandrel-Sill-Vinyl Irving's	29-30 37WES		37	38	39	39	39
Corner Steel	41-56				58	59	59
Drilling Castings	59-60	59-60	59-61	61-60	61S 62N	64N 62W	63-64
Steel Liner - Richie	52-53 54-55	52-53 54-55	52-53 54-55	57-56 55-54	57-56 55	58 56 57 Holes	56-57-58 59
41 FL - Set Backwall Harry							
North Lobby - Ed Brown	Insert glass frames		glass fr[illegible]	glass fr[illegible]	Insert glass [illegible]	Insert glass [illegible]	glass [illegible]
Castings	65	56-57	57	57	58-59	61-60	61-62
B-7-8 FL Steel	Steel +						
Lobby Layout							
Spray Fireproof. DiBona	39-43 40	40	47-49	49 47	49-47	48-50	50-48
Patching Fireproof	39	40	39	40 No Water Stop, 10:45 AM Run 1PM	43	44	44-
Brown Coat	24 SWNE		25	25	25	25	25
White Coat	22		23	23	23	23	24
Vermiculite Scratch	39		39	40	40	46	46
Brandt Tony (22)	27 Steel Channel		28	28	29 Hoist 26H	29	30
Hang Hole Plate Approved?		start w/ Hack [illegible]	24 25 Col Con Damage		24-25 [illegible] B/C		

Sat 8-8 fair	Mon fair 8-10-70	Tues fair 8-11-70	Wed fair 8-12-	Thurs fair 8-13	Fri fair 8-14	Sat fair 8-15	
	40	40	40-43	40-43 44	43-44	X	Taps burned 56
	36-37 36 make 30	36-37	37-38	36 37-	37-38	X	from 4 Elev. Back
		37	37-38	37-38	39	X	Welding of [illegible]
	39	39-40	39-40	39	39	X	Jambs also 55
	35-32	33	34	35	36-37	X	South - 26 - 9 West [illegible] 10 East
	30	30/109	30-31	32	32-33	33	25 ft - [illegible]
	39-NES	39	40	40	40		
	59	59	60	60	61 66	67	
64-63	65N- 63W	65-66	67-66	68-67	64-68	69	
59-58	61-Sills 60 [illegible] 59 59 [illegible]	61-60	62S 60N 61N	60-61-62	65S 64S 63S-62S	65S-64 67S-63N	
	[illegible]	[illegible]					
64 make 62 set	64 make 63 set 62 set	64-63 90	67 make 66-65	67 66-65	69 m-65 67	68-67	
43 E-W	53 E-W 57	51-53	54-53	54-52	57-55	Lobby	Plaster Weld on Jamb Plates
46	47-46	47	47-46	48	48	X	
Plant 22	25	X	26	26	26	X	
Job	24	25	25	25	25	X	
39	47	48	49	49	52	X	Jack Sorrell 849 0451
	31	31	32	33	34	X	Jerry Levers Alcoa
Class 45 [illegible]							Larry Ginbro Cupples

Stairs

Tread/Riser

A-AB-204

205

8-12-70

Unit in 8-12-70. Stops by ...
Waited for George ... for Phones drop
Was ... to 310 unit - 1:15 PM.

449 □ × 450 □

1/2" + 1/4"

1st 200# wt.
2nd 600# wt. } 600# total

Threading unit with Column Counter

(2) 451 □ × 452 □ West Elev

1st - 200#
2nd - 600#

+ 0 17/8

ft Cable - 80 ft
ft Travel - 20 floors

Dick Hoffman

Tom Christensen

47 Bill Borland

1 Hdg 57 East
56 -

MARCH 30-70
April 1
May 2
June 3
July 4
Aug 5
Sept 6

214 - Toilet Plans & Elev 8'0 FF/FC
215 Ceiling Plan Zone 1
218 Ceiling detail
219 Ceiling detail
220 Elev Lobby Typ. & Elev
221 Elev Lobby details 8.0 1/2"
Tenant Ceiling FF/FC 8'7 1/4"

Aug

S	M	T	W	T	F	S
26	27	28	29	30	31	1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31	1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

Floor	L	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	2
Layout		X	X	X	X	X	/	/	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Top Track		X	X	X	X	X			X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Bot Track		X	X	X	X	X			X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Studs		X	X	X	X	X			X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Core		-		X						X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Sheetrock										X	/	/	/	/	/	/	/	/	/	/	/	/	/	/	/	/
Bucks Stair S Elev E Hum P		/	/	/	/	/	/	/	/	S E	S /	S /	9 /	S /	S /	/	/	/	/	/	/	/	/	/	/	/
Chasewall																										
2½ Studs																										
H-D Metal										X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
H-D Core										X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
H-D Sheet Rock ⅝										X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	
H-D Sheet Rock R 5/8										X	X	X	X	X	X	X	X	X								
H-D Bucks										X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Protection Sheetrock Ceiling		X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Doors																										
Soffit																										
Corner Bead																										
Rigid Insul																										
Tape																										
Hardware																										
Bath Fixt																										
Sheetrock ½ W A									X	X	X	X	X	X	X	X	X	X	X							
Sheetrock ⅝ E R								X	X	X	X	X	X	X	X	X										

27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	53	54	55	56	57	58	59
X	X	X	X	X	X	X	X	X	X	X	X	X	X	\	X		X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
X	X	X	X	X	X	X	X	X	X	X	X	X	X		X		X	X	X	X	X	X	X	X	X	X						
X	X	X	X	X	X	X	X	X	X	X	X	X	X		X																	
X	X	X	X	X	X	X	X	X	X	X																						
X	X	X	X	X	X																											
/	/	/																														
/	/	/	/	/	/																											
X	X	X	X	X	X	X	X	X	X	X	X	X	X																			
X	X	X	X	X	X	X	X	X	X	X	X	X	X																			
X	X	X	X	X	X	X	X	X	X	X																						
X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X

Part Height Up to	Size of Gyp Plank	'J' Runner Gauge	H. Stud # 7.5 PCF Exp	Channels 10 PCF 41.42	15 PCF 75-76-107-108
11'-0	2"X16"	20	24 Green	24	18
11'-6	2X16	20	22 Blue	22	16
12'-0	2X16	20	20 Red	20	14
12'-6	2X12	20	18 Yellow	18	16
13'-0	2X12	20	18	18	14
13'-6	2X12	20	16 Black	16	14
14'-0	2X12	20	14	14	12
14'-6	2½X12	16	18	18	16
15'-0	2½X12	16	16	16	16
15'-6	2½X12	16	14	14	14
16'-0	2½X12	16	14	14	14

Bar Joists / Floor A
N-S-30 - E-W-14

A Jackson EX-2-4330

Badger -
Al Siderberg motors
Ni-9-6400

Hert. FL-9-6985

Amplast Doris MO-5-0522

Charlie Hoffman
Emery Rock Art

#6 Shaft 7 hours
#7 Shaft 8-9 hours.

ROYAL
669
Made In America
U.S.A.

Baffles Vertical

1-2-3-4-14-24-36-46-56 57 58 59

Westwood Paper →
384 Lafayette St

Robert Grant
9828 BB "N"

[illegible] Hill
20-4003

Bob Tell



Office - 267-7680 x28/[illegible]

Atlas Port Morris Hugh Reilly
914-633-6300
597-9500

Craft Art 291-1116 [illegible]
John [illegible] 267-3210 [illegible]

[illegible] Steel - 937-2700

[illegible] - 732-5222

TONY AVOLA - TISHMAN

LEW GUADAGNO

WRITE IT - DONT SAY IT

CIRCLE FLOOR CO., INC.

UNDERSIDE OF

7TH, 9TH, 41ST, 43RD, 75TH, 108TH, 110T

PLENUM ROOF SLAB ELEV. 242 -

PA 36
12-54

THE PORT OF NEW YORK AUTHORITY

A-59211

10-19 1970

W. Schleis
To: R. O'Hara

From: PAUL M. CAVANAGH — 30 Church Street Ext. (61) 39

I-3 – Nos for Contracts 113-115

Contract 113

Spraying	42-51
Clean-up	51-56
Punch-List	56-87

Contract 115

Black Iron	87-88
Ceiling Tile	125-126

- - - - - - - - - - - - - - - - - -

Narrative Card
Floor # + I-J

PA 36
12-54

THE PORT OF NEW YORK AUTHORITY

A-88211

To: SCHLIEF Room No.

From: Call Room No.

Date 7/7/70

Lou

ZACCARDO 10 AM

215-699-5270

Laminators Inc -

after 8 AM

Tomorrow

MINORU YAMASAKI AND ASSOCIATES
350 WEST BIG BEAVER ROAD TROY, MICHIGAN 48084

Craft Architectural Metals Corp.
120 Fairchild Avenue
Plainview, L.I.,
New York 11803

Attn: Mr. Charles Senzel

FORM 110 8M 7-69

PA 26
12-54

THE PORT OF NEW YORK AUTHORITY

A-55211

19

To:

From: E. BOLAND — 53 Dey Street Ext. (61) 61

1/8" = .01
1/4" = .02
ETC.

1" = .08
2" = .17
3" = .25
4" = .33
5" = .42
6" = .50

7" = .58
8" = .67
9" = .75
10" = .83
11" = .92
12" = 1.00

.69
.19

PA 86 12-64 THE PORT OF NEW YORK AUTHORITY A-89211

7/10 19 70

To: W. SCHLEIF/R. O'HARA

From: E. BOLAND — 53 Dey Street Ext. (61) 61

LEROY PORTER
OR PHIL GOZ
620-7929

CONTR. 108
CALL. 115
FOR LATEST INFO
ON THESE CONTRACTS

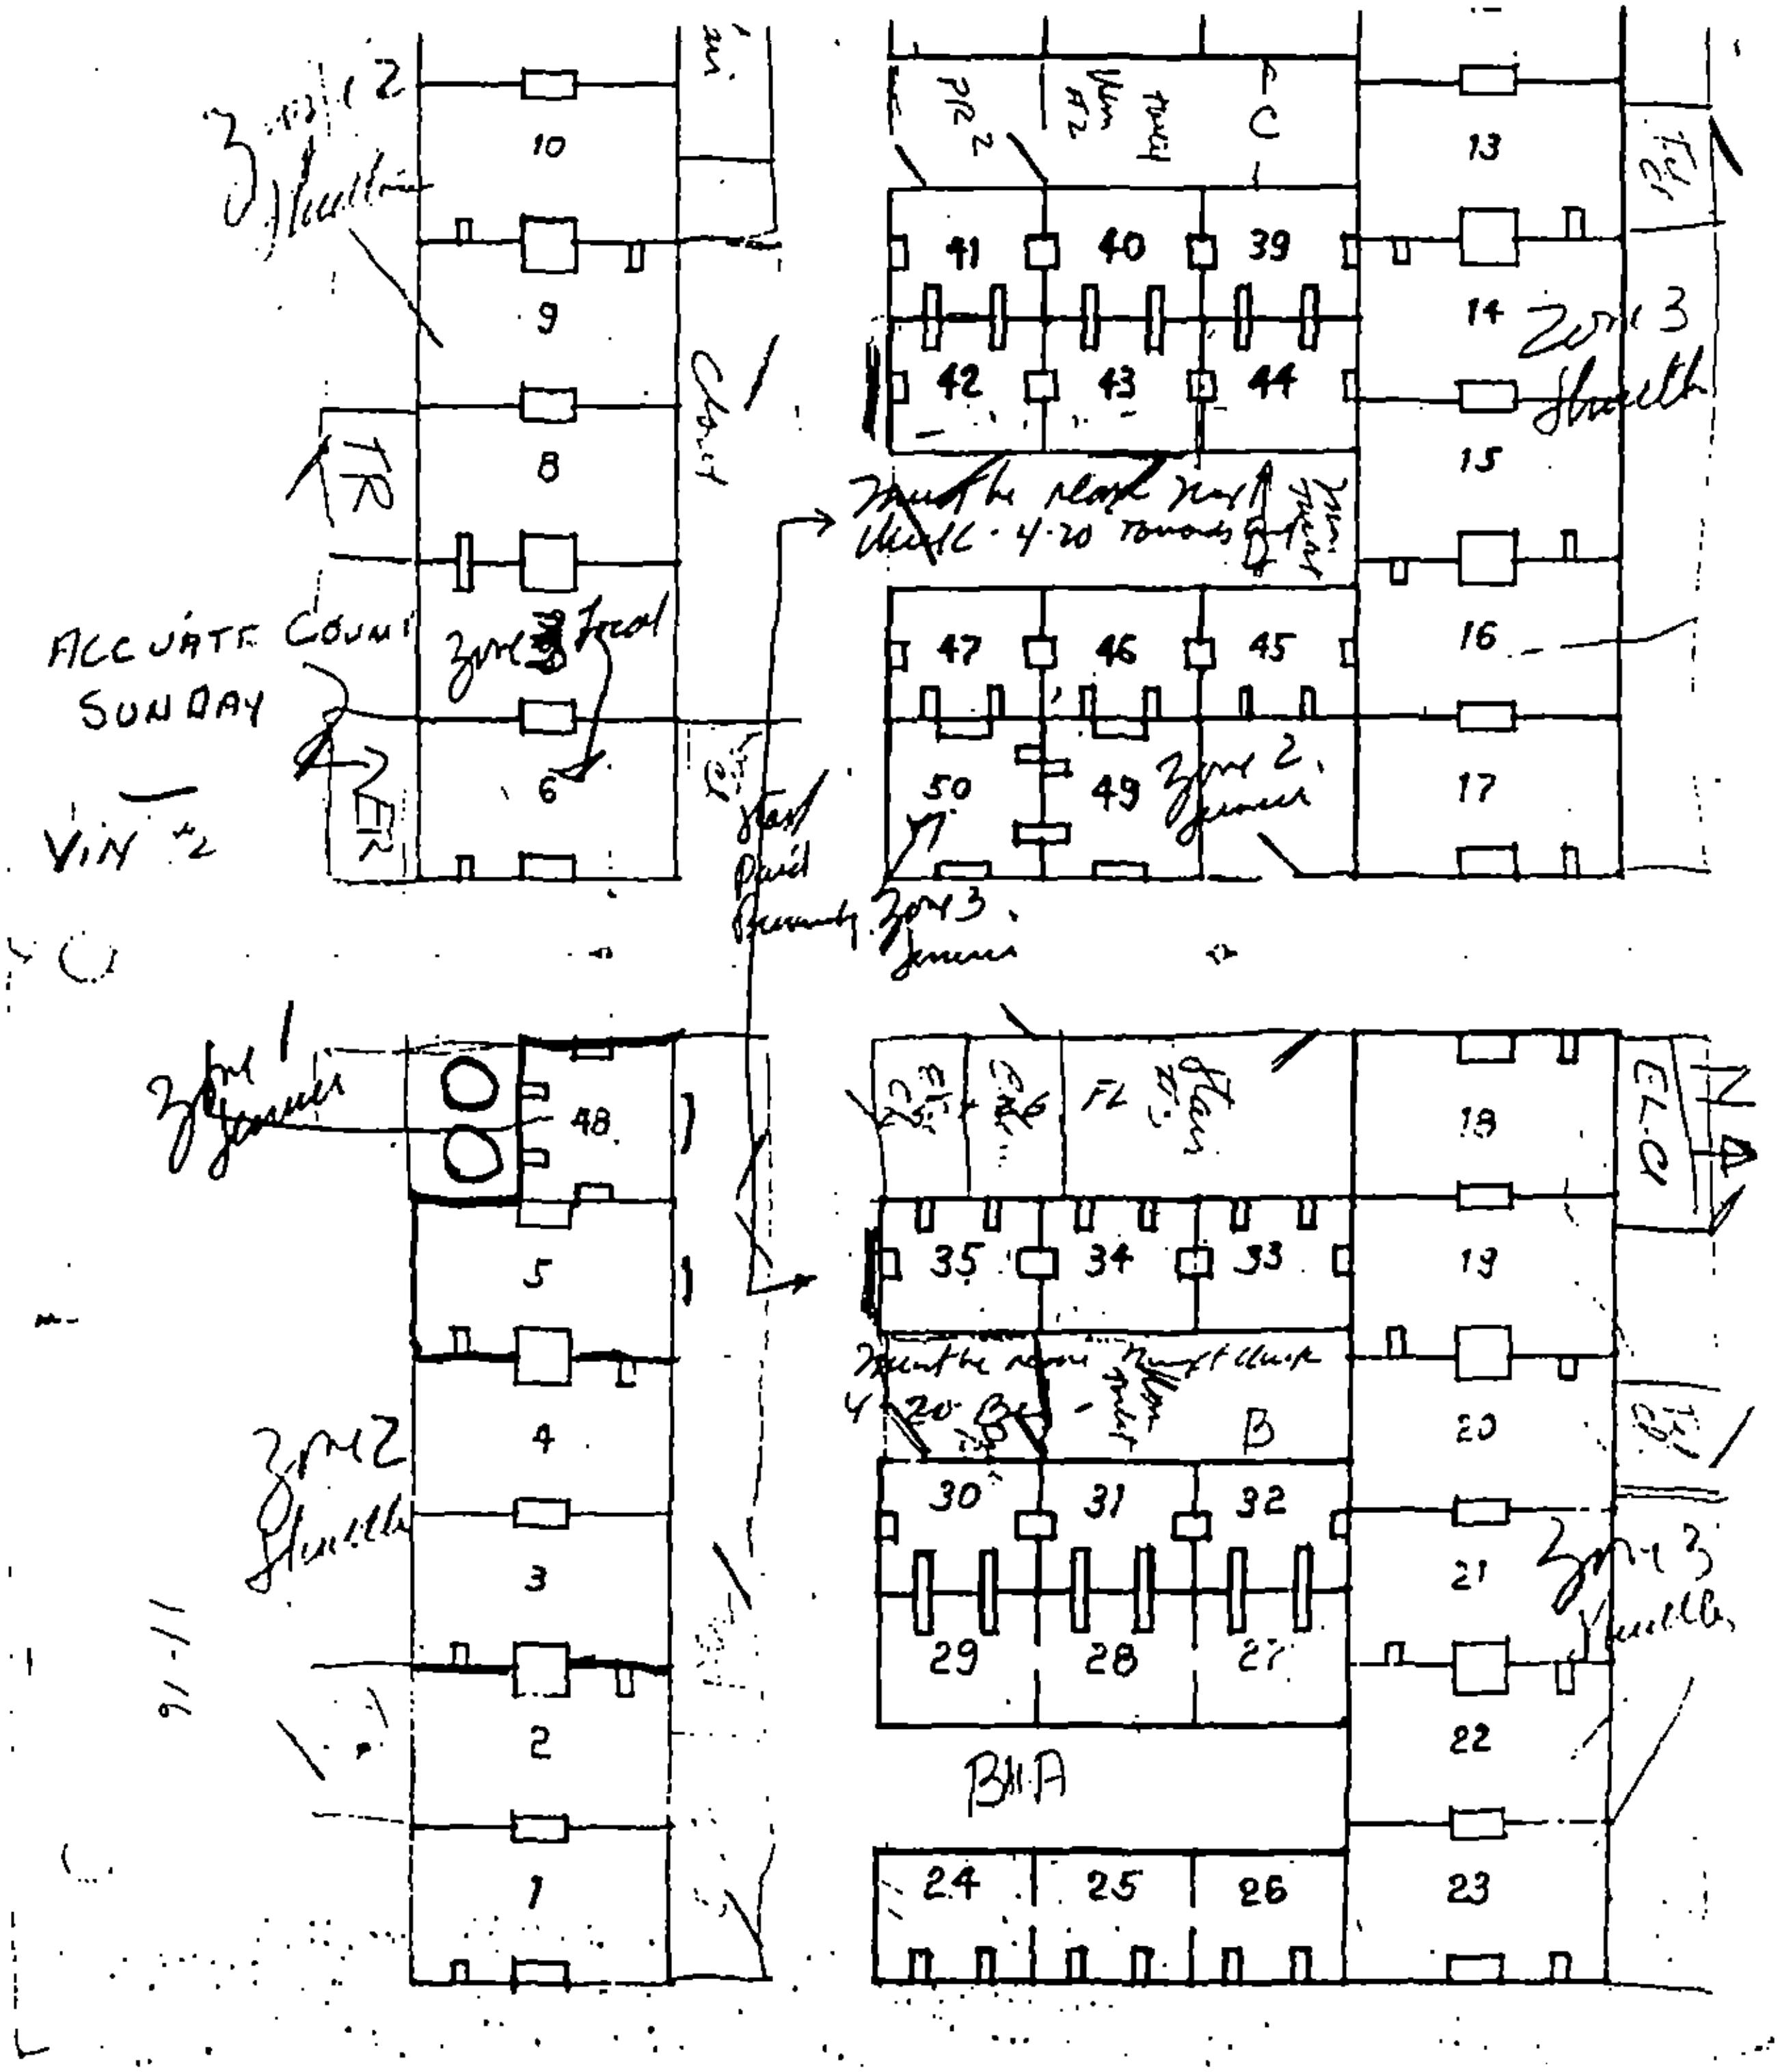

ACCURATE COUNT
SUNDAY
VIN #2
Zone 3 Shuttle
Zone 2 Shuttle
Zone 1 Jennie
Zone 2 Jennie
Zone 3 Jennie
TR
ER
C
B
BHA
FL
1
2
3
4
5
6
8
9
10
13
14
15
16
17
18
19
20
21
22
23
24
25
26
27
28
29
30
31
32
33
34
35
39
40
41
42
43
44
45
46
47
48
49
50

TOWER A ZONE I FLOOR 1

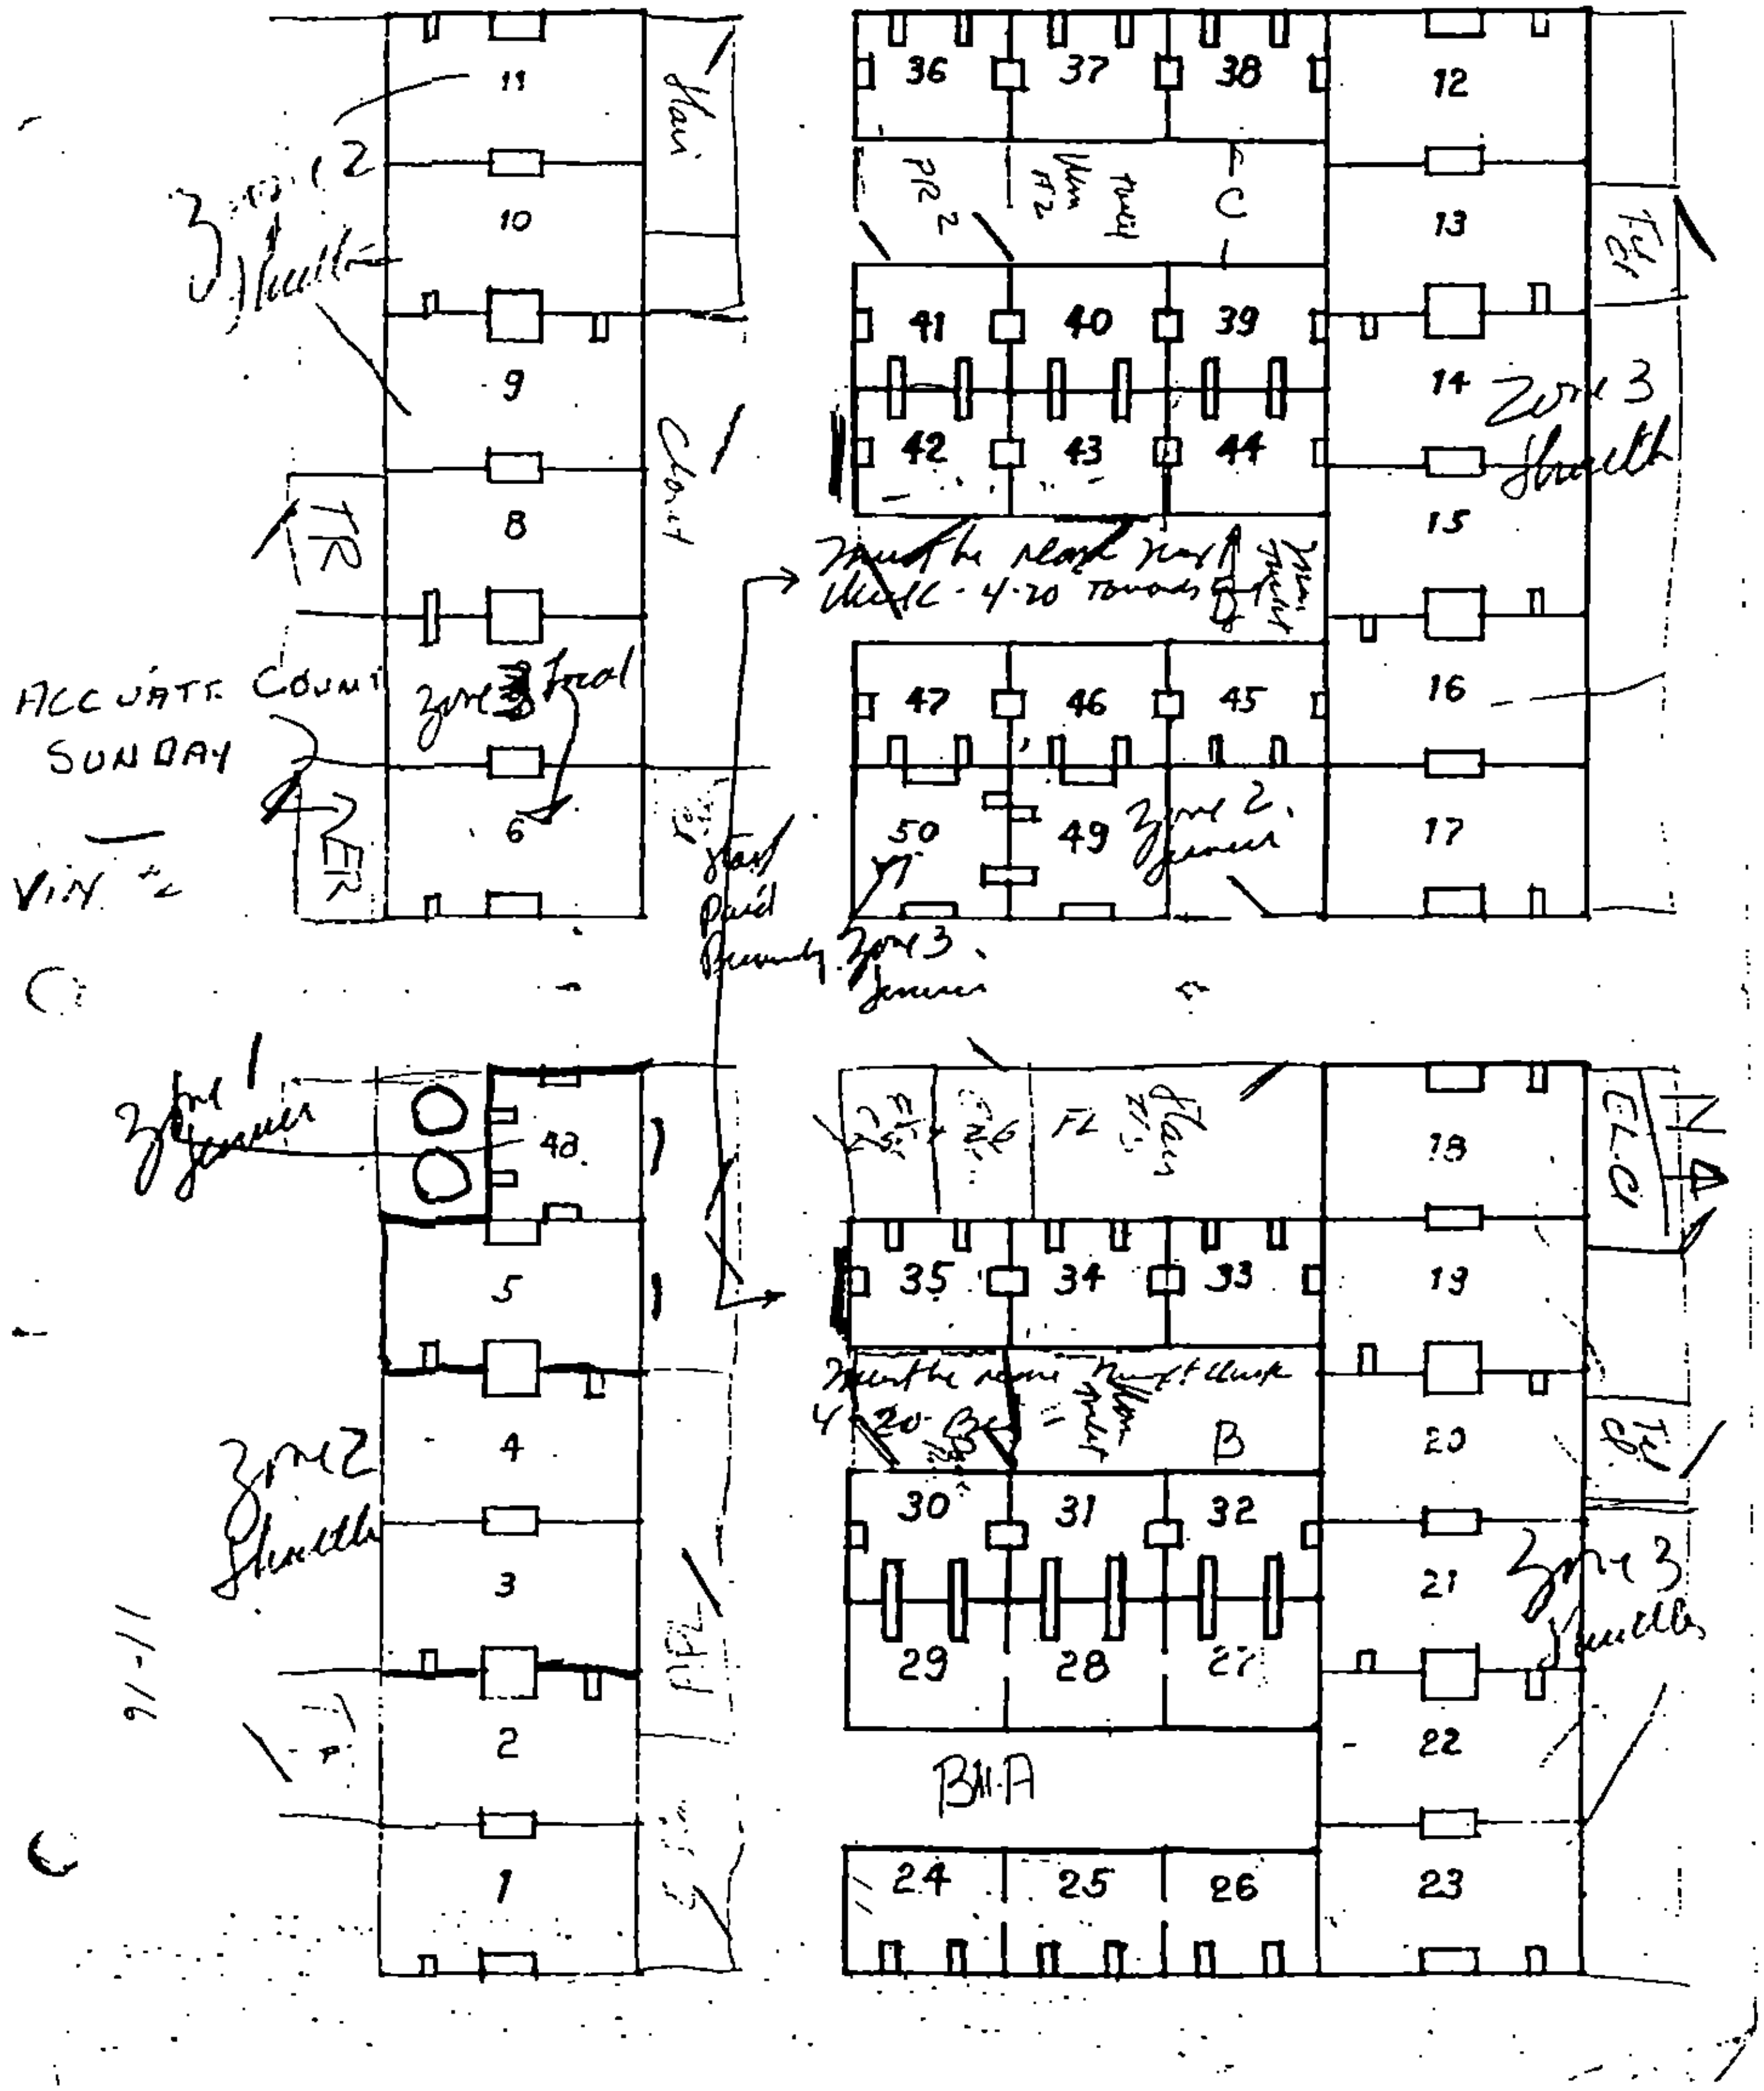

13.07 WORKMANSHIP

1. The Contractor shall completely shield adjacent finished materials including all aluminum or other ornamental metal, cut stone, and all other finished work from splashing by droppings and misdirected sprayed-on fireproofing material being applied under the Contract. Material which may splash against the ornamental metal, cut stone, and other exposed finished work shall be immediately cleansed from the metal, stone or other material with water by the Contractor.

2. Maintaining such adjacent finished materials free from fireproofing material shall be the responsibility of the Contractor. Adjacent and other materials damaged due to improper protection or negligence on the part of the Contractor shall be replaced by him at his own expense.

3. The Contractor shall coordinate with all other trades as may be directly or indirectly involved in the work and shall schedule his work in such manner as to avoid delay in the progress of the work.

4. The sprayed-on fireproofing and sprayed-on insulation, when completed, shall be free from seams, staging breaks, holes, spalls, cracks, flaking and dusting action, and other defects of any kind.

13.08 *CLEANING AND PROTECTION*

1. Upon completion of the application of each coat of spray-on material, on each respective floor, or in each respective area, as may be directed by the Engineer, the Contractor shall remove all debris from floors, walls, and other surfaces, and shall collect and deposit such debris in floor containers which shall be provided by the Authority in each area or on each floor where work is being performed. Debris will be removed by others.

2. During the spray-on operations, floors beneath and around machines, water containers, and mixing boxes shall be protected with waterproofed coverings. All metal and other work adjoining the plastering and spray-on operations, including finished concrete floors, shall be protected and shall be cleansed of all spray-on material and any soiling as may occur, immediately upon completion of the finish coats.

3. Upon completion of the work in any areas, or on any floors, the area or floor shall be scraped and left broom clean. All equipment shall be removed when and as directed by the Engineer.
